



ENGINEERS, INC.

CONSTRUCTION INSPECTION REPORT

Project: Knudson Cove Harbor				Report No: Pool – 005		
File No: 062010.05 C-3				Date: February 2, 2009		
Consultant: PND Engineers, Inc.				Day of the Week: Monday		
WEATHER						
	Bright Sun	Clear	Overcast	Rain X	Snow	Other
TEMP	Below 0	0-32	32-50 X	50-70	70-85	Over 85
WIND	Still X	Mod	High	Comments:		
HUMIDITY	Dry	Mod X	Humid	Comments:		
CONTACTS						
Name of Contractor		Non-Manual		Manual		Remarks
Pool Engineering		1		4		
FIELD ACTIVITIES						
<p>Contractor placed the gangway in position. The gangway hinge assembly did not have the 1/8" UHMW isolation washers, as specified in the Contract Documents. This was discussed with the Contractor, and he said they will be added at a later time. The skid base plate/guide assembly was temporarily nailed in position and, will be monitored over several tide cycles to ensure correct placement.</p> <p>The Contractor removed two more existing timber piles and another 65' section of existing float. Headwalk float unit 2 was installed per drawings.</p> <p>Pile H2 was then driven with the vibratory hammer to almost full penetration. The Contractor stopped pile driving do to lack of light.</p>						
PHOTOS TAKEN						

CONSTRUCTION INSPECTOR: Lance Greer


DATE: February 2, 2009



Photograph No. 1

Description:

Gangway in position

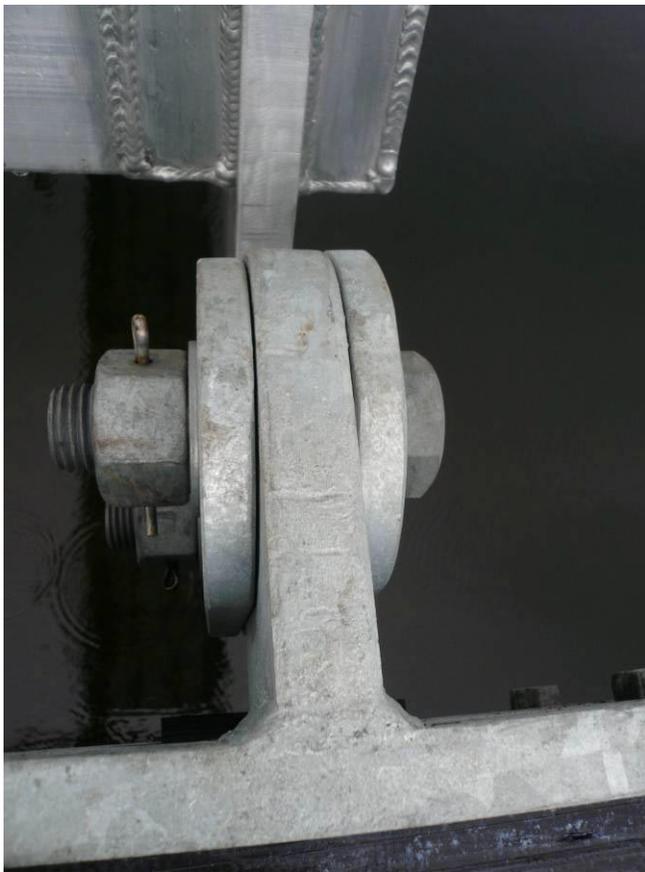

Photograph No. 2

Description:

Gangway hinge assembly w/o
isolation washers
