

ID	Task Name	Duration	Start	Finish	Predecessors	Quarter																							
						1st Quarter		2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			
						Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	Perryville Barge Landing and Launch Ramp Desi	2368 days	Fri 12/24/04	Tue 1/21/14																									
2	Kickoff Meeting	1 day	Thu 2/17/11	Thu 2/17/11																									
3	Develop PMP	55 days	Wed 2/23/11	Tue 5/10/11																									
11	Site Visit	3 days	Mon 4/11/11	Wed 4/13/11																									
12	Trip Report	18 days	Thu 4/14/11	Mon 5/9/11	11																								
13	Public Involvement	90 days	Fri 12/24/04	Thu 4/28/05																									
15	Engineering and Design	185 days	Thu 3/31/11	Wed 12/14/11																									
30	Environmental (EA)	195 days	Tue 5/10/11	Mon 2/6/12																									
39	Real Estate	297 days	Thu 2/24/11	Fri 4/13/12																									
44	Cost Estimate	265 days	Tue 8/9/11	Mon 8/13/12																									
45	50% Estiamte	39 days	Tue 8/9/11	Fri 9/30/11	19																								
46	IGE	5 days	Tue 8/7/12	Mon 8/13/12	45,64																								
47	BCOE Review	18 days	Tue 5/29/12	Thu 6/21/12																									
48	Review	10 days	Tue 5/29/12	Mon 6/11/12	29,38,41,58																								
49	Incorporate Comments	5 days	Tue 6/12/12	Mon 6/18/12	48																								
50	Certificate	3 days	Tue 6/19/12	Thu 6/21/12	49																								
51	MOA Signed Between Tribe/USACE	15 days	Fri 5/11/12	Thu 5/31/12																									
52	Support Agreement Signed	10 days	Fri 6/1/12	Thu 6/14/12	51																								
53	Receiving Funds from Native Village of Perryvill	1 day	Fri 6/15/12	Fri 6/15/12	52																								
54	Contracting - IFB	243 days	Tue 10/25/11	Thu 9/27/12																									
55	Description of Scope	1 day	Tue 10/25/11	Tue 10/25/11	17FS+185 days																								
56	Sources Sought	22 days	Tue 11/1/11	Wed 11/30/11	55																								
57	2579	2 days	Thu 12/1/11	Fri 12/2/11	56																								
58	Front End	9 days	Fri 5/11/12	Wed 5/23/12	57																								
59	Prepare for Legal Review	3 days	Fri 6/22/12	Tue 6/26/12	58,50,47																								
60	Legal Review	4 days	Wed 6/27/12	Mon 7/2/12	59																								
61	Peer Review	3 days	Wed 6/27/12	Fri 6/29/12	59																								
62	Advertise	10 days	Mon 7/2/12	Fri 7/13/12	61,53																								
63	Solicitation	15 days	Mon 7/16/12	Fri 8/3/12	62																								
64	Pre-proposal Conference	1 day	Mon 8/6/12	Mon 8/6/12	62FS+15 days																								
65	Bid Opens	1 day	Mon 8/6/12	Mon 8/6/12	63																								
66	Verify Bids	10 days	Tue 8/7/12	Mon 8/20/12	65																								
67	Prepare Award Package	10 days	Tue 8/21/12	Mon 9/3/12	66																								
68	Award	3 days	Tue 9/4/12	Thu 9/6/12	67																								
69	Bonds	10 days	Fri 9/7/12	Thu 9/20/12	68																								
70	Legal Review	4 days	Fri 9/21/12	Wed 9/26/12	69																								
71	NTP	1 day	Thu 9/27/12	Thu 9/27/12	70																								
72	Construction	276 days	Fri 11/9/12	Fri 11/29/13																									
73	Pre-construction Conference	1 day	Fri 11/9/12	Fri 11/9/12	71FS+30 days																								
74	Construction	260 days	Mon 11/12/12	Fri 11/8/13	73																								
75	Final Inspection	1 day	Mon 11/11/13	Mon 11/11/13	74																								
76	Project closeout	14 days	Tue 11/12/13	Fri 11/29/13	75																								
77	Project Complete	37 days	Mon 12/2/13	Tue 1/21/14																									
78	Physical Closeout	3 days	Mon 12/2/13	Wed 12/4/13	76																								
79	Transfer of Remaining Funds	30 days	Thu 12/5/13	Wed 1/15/14	78																								
80	Fiscal Closeout	3 days	Thu 1/16/14	Mon 1/20/14	79																								
81	Project Closed Out	1 day	Tue 1/21/14	Tue 1/21/14	80																								

Project: Perryville Design Schedule
Date: Tue 5/29/12

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone


Page 1

	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Q
Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Project: Perryville Design Schedule
Date: Tue 5/29/12

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

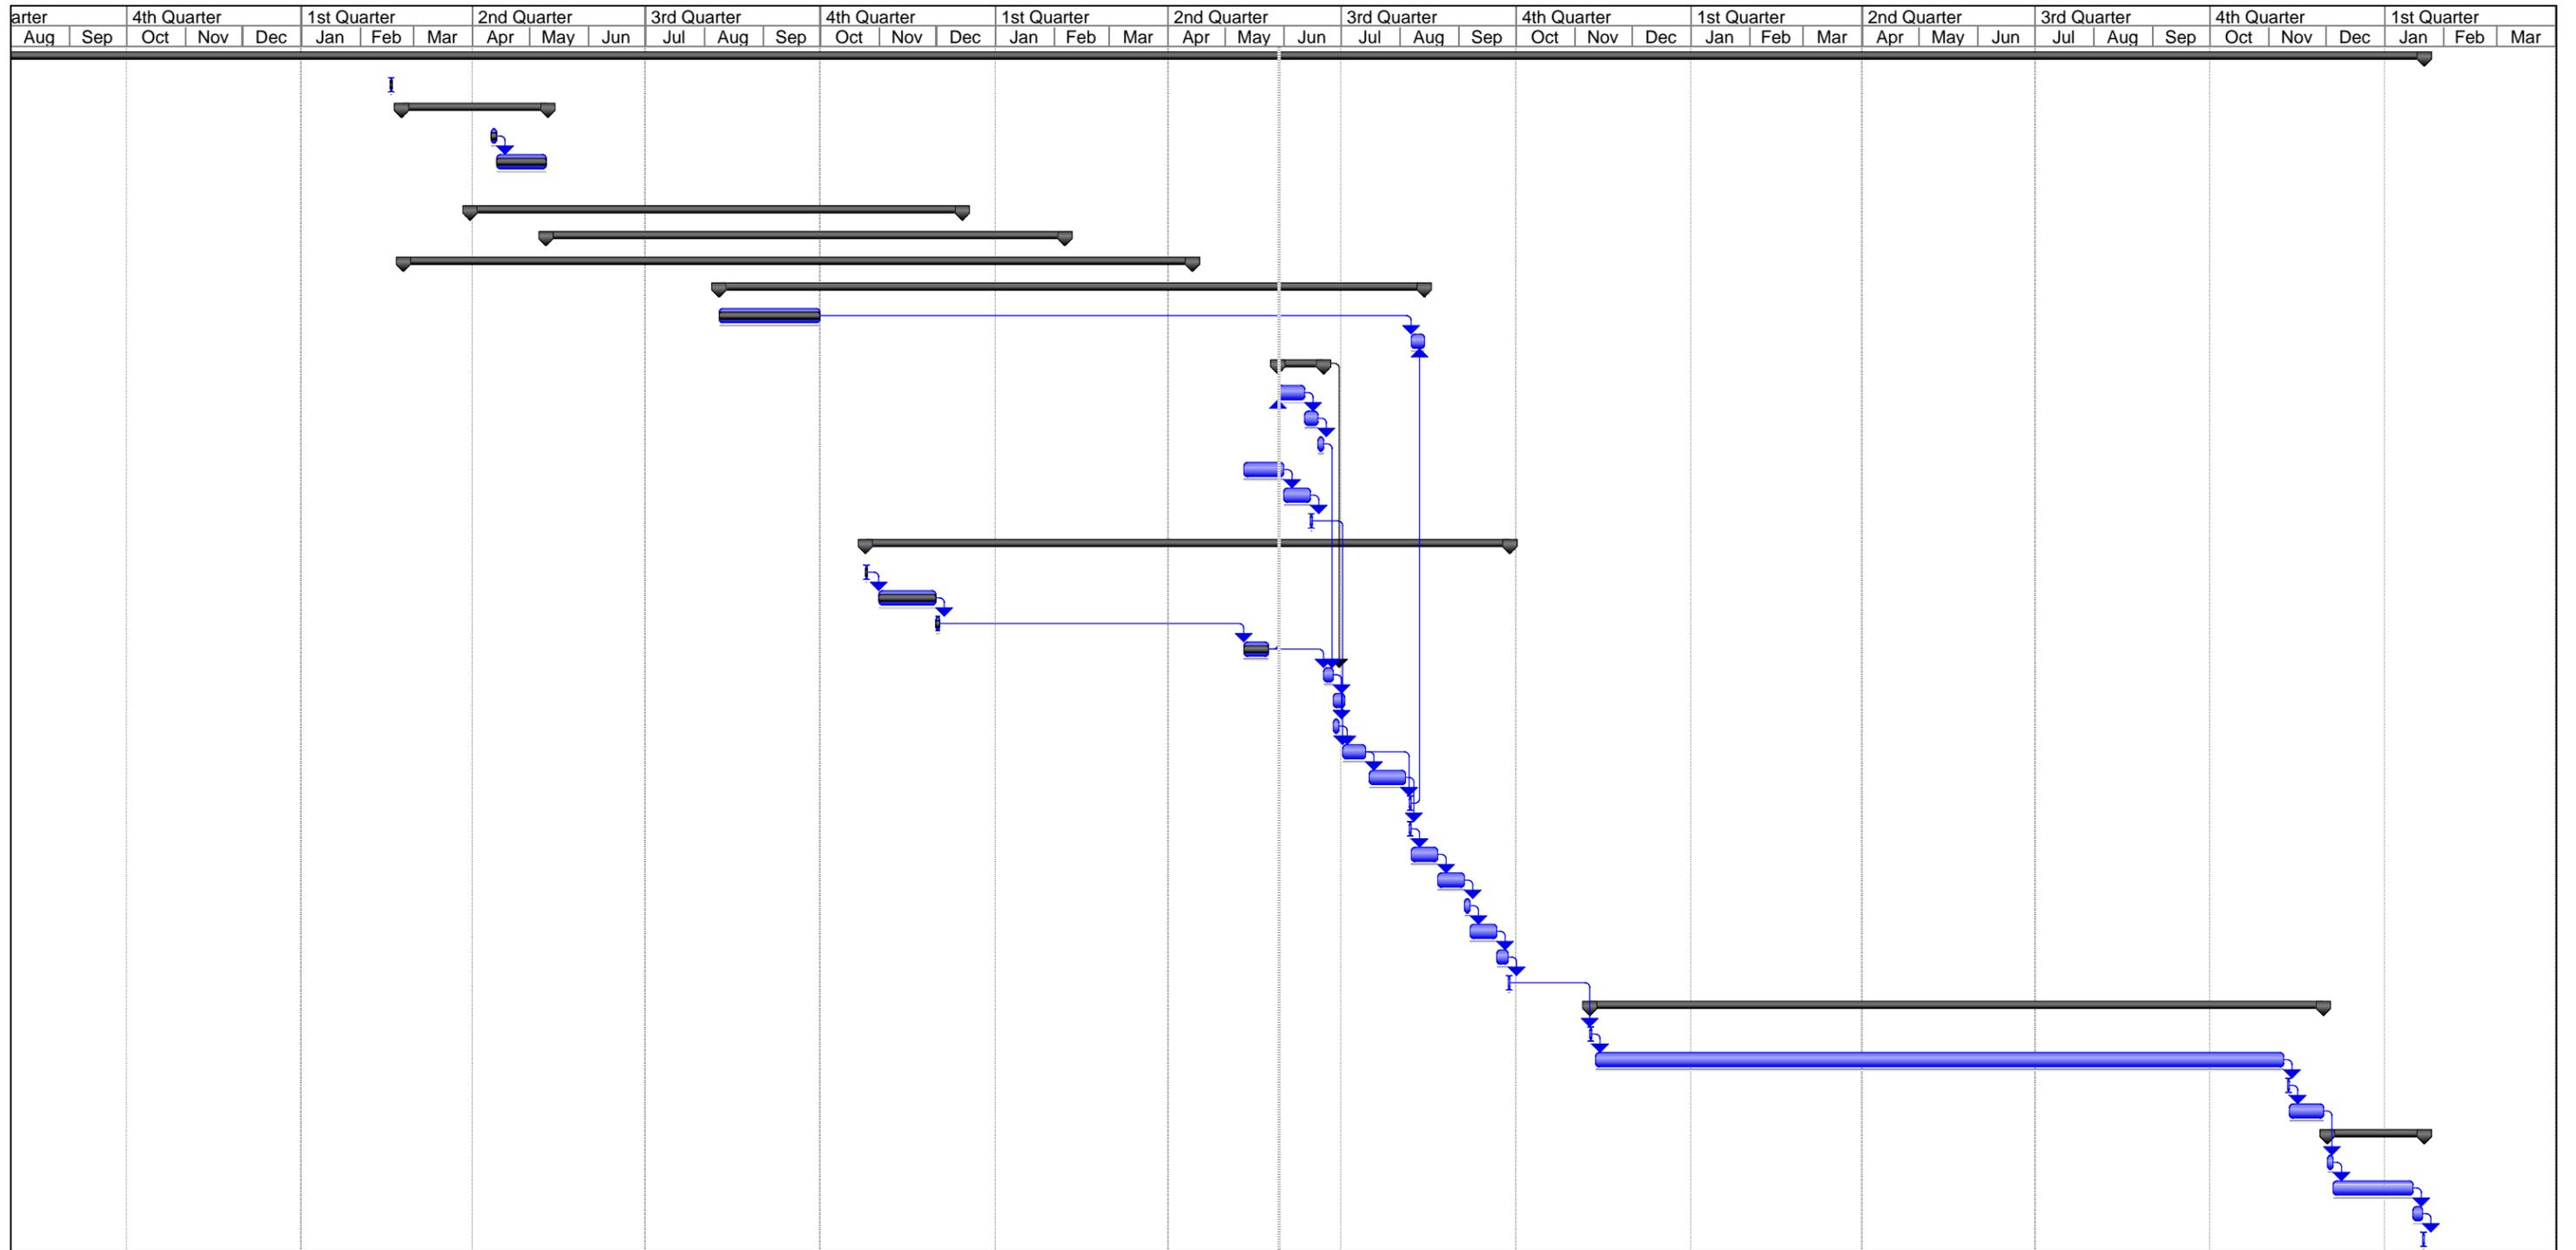

Project: Perryville Design Schedule
Date: Tue 5/29/12

- Task Progress
- Split Milestone
- Summary
- Project Summary
- External Tasks
- External Milestone
- Deadline
