


ID	Task Name	Duration	Start	Finish	1st Quarter			2nd Quarter			3rd Quarter				
					Jan	Feb	Mar	Apr	May	Jun	Jul				
1	<b>Eek Barge Landing</b>	<b>458 days</b>	<b>Tue 2/2/10</b>	<b>Thu 11/3/11</b>											
2	Kickoff Meeting	1 day	Tue 2/2/10	Tue 2/2/10											
3	<b>Develop PMP</b>	<b>74 days</b>	<b>Wed 2/3/10</b>	<b>Mon 5/17/10</b>											
11	Site Visit	1 day	Mon 6/21/10	Mon 6/21/10											
12	Trip Report	14 days	Tue 6/22/10	Fri 7/9/10											
13	<b>Public Involvement</b>	<b>9 days</b>	<b>Mon 6/21/10</b>	<b>Thu 7/1/10</b>											
15	<b>Engineering and Design</b>	<b>279 days</b>	<b>Tue 6/22/10</b>	<b>Fri 7/15/11</b>											
16	Surveys and Mapping	72 days	Mon 7/12/10	Tue 10/19/10											
17	Site Development	12 days	Tue 6/22/10	Wed 7/7/10											
18	Design	45 days	Tue 1/4/11	Mon 3/7/11											
19	50% Design for PDT Review	5 days	Tue 3/8/11	Mon 3/14/11											
20	Incorporate Comments	5 days	Tue 3/15/11	Mon 3/21/11											
21	Meeting with Customer on Design	1 day	Tue 3/22/11	Tue 3/22/11											
22	Plans & Specs	45 days	Wed 3/23/11	Tue 5/24/11											
23	Plans&Specs, Incorporate Comments	5 days	Wed 5/25/11	Tue 5/31/11											
24	Final Design Package for PDT Review	5 days	Wed 6/1/11	Tue 6/7/11											
25	Review (ITR)	14 days	Wed 6/8/11	Mon 6/27/11											
26	Incorporate Comments	5 days	Thu 7/7/11	Wed 7/13/11											
27	PDT Review of Comments Incorporated	1 day	Thu 7/14/11	Thu 7/14/11											
28	Final Design Complete	1 day	Fri 7/15/11	Fri 7/15/11											
29	<b>Environmental (EA)</b>	<b>195 days</b>	<b>Wed 1/5/11</b>	<b>Tue 10/4/11</b>											
30	Prepare documents	15 days	Wed 1/5/11	Tue 1/25/11											
31	SHPO	30 days	Wed 1/26/11	Tue 3/8/11											
32	F&W Coordination	30 days	Wed 7/13/11	Tue 8/23/11											
33	Section 404(b)(1) Analysis	30 days	Wed 1/26/11	Tue 3/8/11											
34	Record of Decision	30 days	Wed 1/26/11	Tue 3/8/11											
35	Section 103 Evaluation	30 days	Wed 1/26/11	Tue 3/8/11											
36	Statement of Findings	30 days	Wed 1/26/11	Tue 3/8/11											
37	CZM Consistency	60 days	Wed 7/13/11	Tue 10/4/11											
38	Draft Final	80 days	Wed 1/26/11	Tue 5/17/11											
39	Pre-NEPA Meeting with Customer	1 day	Wed 5/18/11	Wed 5/18/11											
40	Public Review	30 days	Wed 7/13/11	Tue 8/23/11											
41	Sign FONSI	6 days	Wed 8/24/11	Wed 8/31/11											
42	<b>Real Estate</b>	<b>375 days</b>	<b>Wed 2/3/10</b>	<b>Tue 7/12/11</b>											
43	Ownership Identification	15 days	Wed 2/3/10	Tue 2/23/10											
44	<b>Obtain Permits for Construction</b>	<b>135 days</b>	<b>Wed 1/5/11</b>	<b>Tue 7/12/11</b>											
45	From City	135 days	Wed 1/5/11	Tue 7/12/11											
46	State Tidelands	135 days	Wed 1/5/11	Tue 7/12/11											
47	<b>Cost Estimate</b>	<b>45 days</b>	<b>Tue 3/15/11</b>	<b>Mon 5/16/11</b>											

Project: Eek Draft Schedule 0.45mpp Date: Wed 11/17/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	1st Quarter			2nd Quarter			3rd Quarter
					Jan	Feb	Mar	Apr	May	Jun	Jul
48	Develop Construction Cost	45 days	Tue 3/15/11	Mon 5/16/11							
49	<b>Project Complete</b>	<b>46 days</b>	<b>Thu 9/1/11</b>	<b>Thu 11/3/11</b>							
50	Publication/Reproduction	5 days	Thu 9/1/11	Wed 9/7/11							
51	Copies to Customer and Community	5 days	Thu 9/8/11	Wed 9/14/11							
52	Physical Closeout	3 days	Thu 9/15/11	Mon 9/19/11							
53	Transfer of Remaining Funds	30 days	Tue 9/20/11	Mon 10/31/11							
54	Fiscal Closeout	3 days	Tue 11/1/11	Thu 11/3/11							

Project: Eek Draft Schedule 0.45mpp Date: Wed 11/17/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



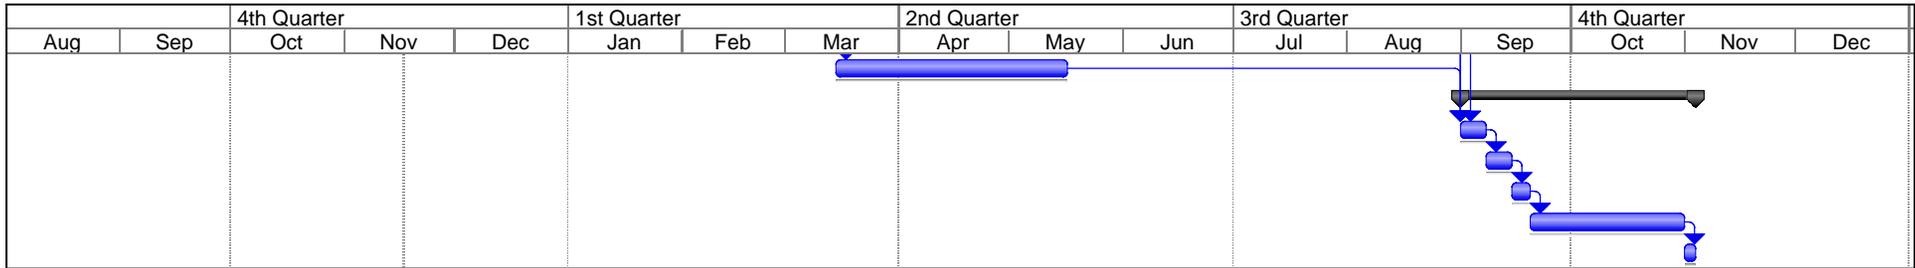

Project: Eek Draft Schedule 0.45mpp  
 Date: Wed 11/17/10

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
