


ID	Task Name	Duration	Start	Finish	Predecessors	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	<b>Eek Barge Landing</b>	<b>588 days</b>	<b>Tue 2/2/10</b>	<b>Thu 5/3/12</b>											
2	Kickoff Meeting	1 day	Tue 2/2/10	Tue 2/2/10											
3	<b>Develop PMP</b>	<b>74 days</b>	<b>Wed 2/3/10</b>	<b>Mon 5/17/10</b>											
11	Site Visit	1 day	Mon 6/21/10	Mon 6/21/10											
12	Trip Report	14 days	Tue 6/22/10	Fri 7/9/10	11										
13	<b>Public Involvement</b>	<b>9 days</b>	<b>Mon 6/21/10</b>	<b>Thu 7/1/10</b>											
15	<b>Engineering and Design</b>	<b>439 days</b>	<b>Tue 6/22/10</b>	<b>Fri 2/24/12</b>											
16	Surveys and Mapping	72 days	Mon 7/12/10	Tue 10/19/10	12,17										
17	Site Development	12 days	Tue 6/22/10	Wed 7/7/10	11										
18	Design	49.5 days	Mon 1/3/11	Tue 9/6/11	32										
19	50% Design for PDT Review	5 days	Tue 9/6/11	Mon 9/12/11	18										
20	50% Design for Chief Review	5 days	Tue 9/6/11	Mon 9/12/11	18										
21	Incorporate Comments	5 days	Tue 10/4/11	Mon 10/10/11	20FS+15 days										
22	Meeting with Customer on Design	1 day	Mon 10/31/11	Mon 10/31/11	21										
23	Plans & Specs	25 days	Thu 12/15/11	Wed 1/18/12	22,46										
24	Plans&Specs, Incorporate Comments	5 days	Thu 1/19/12	Wed 1/25/12	23										
25	Final Design Package for PDT Review	5 days	Thu 1/26/12	Wed 2/1/12	24										
26	Review (ITR)	10 days	Thu 2/2/12	Wed 2/15/12	25										
27	Incorporate Comments	5 days	Thu 2/16/12	Wed 2/22/12	26										
28	PDT Review of Comments Incorporated	1 day	Thu 2/23/12	Thu 2/23/12	27										
29	Final Design Complete	1 day	Fri 2/24/12	Fri 2/24/12	28										
30	<b>Chemical Sampling</b>	<b>43 days</b>	<b>Mon 6/6/11</b>	<b>Wed 8/3/11</b>											
35	<b>Environmental (EA)</b>	<b>77 days</b>	<b>Wed 9/7/11</b>	<b>Thu 12/22/11</b>											
36	Prepare documents	10 days	Wed 9/7/11	Tue 9/20/11	18,32										
37	SHPO	30 days	Wed 9/21/11	Tue 11/1/11	36										
38	F&W Coordination	30 days	Wed 9/21/11	Tue 11/1/11	36										
39	Section 404(b)(1) Analysis	30 days	Wed 9/21/11	Tue 11/1/11	36										
40	Record of Decision	30 days	Wed 9/21/11	Tue 11/1/11	36										
41	Section 103 Evaluation	30 days	Wed 9/21/11	Tue 11/1/11	36										
42	Statement of Findings	30 days	Wed 9/21/11	Tue 11/1/11	36										
43	CZM Consistency	60 days	Wed 9/21/11	Tue 12/13/11	36										
44	Draft Final	30 days	Wed 9/21/11	Tue 11/1/11	36										
45	Pre-NEPA Meeting with Customer	1 day	Wed 11/2/11	Wed 11/2/11	44										
46	Public Review	30 days	Thu 11/3/11	Wed 12/14/11	45										
47	Sign FONSI	6 days	Thu 12/15/11	Thu 12/22/11	46										
48	<b>Real Estate</b>	<b>494 days</b>	<b>Wed 2/3/10</b>	<b>Mon 12/26/11</b>											
49	Ownership Identification	15 days	Wed 2/3/10	Tue 2/23/10	2										
50	<b>Obtain Permits for Construction</b>	<b>115 days</b>	<b>Tue 7/19/11</b>	<b>Mon 12/26/11</b>											
51	From City - Corporation	115 days	Tue 7/19/11	Mon 12/26/11	32										
52	State Tidelands	115 days	Tue 7/19/11	Mon 12/26/11	32										
53	<b>Cost Estimate</b>	<b>127 days</b>	<b>Tue 9/6/11</b>	<b>Wed 2/29/12</b>											
54	50% CWE	26 days	Tue 9/6/11	Tue 10/11/11	19										
55	95% CWE	10 days	Thu 2/16/12	Wed 2/29/12	26										
56	<b>Project Complete</b>	<b>46 days</b>	<b>Thu 3/1/12</b>	<b>Thu 5/3/12</b>											
57	Publication/Reproduction	5 days	Thu 3/1/12	Wed 3/7/12	27,47,52,55										
58	Copies to Customer and Community	5 days	Thu 3/8/12	Wed 3/14/12	57										
59	Physical Closeout	3 days	Thu 3/15/12	Mon 3/19/12	58										
60	Transfer of Remaining Funds	30 days	Tue 3/20/12	Mon 4/30/12	59										
61	Fiscal Closeout	3 days	Tue 5/1/12	Thu 5/3/12	60										

Project: Eek Draft Schedule 0.45mpp  
Date: Thu 1/5/12

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

Page 1

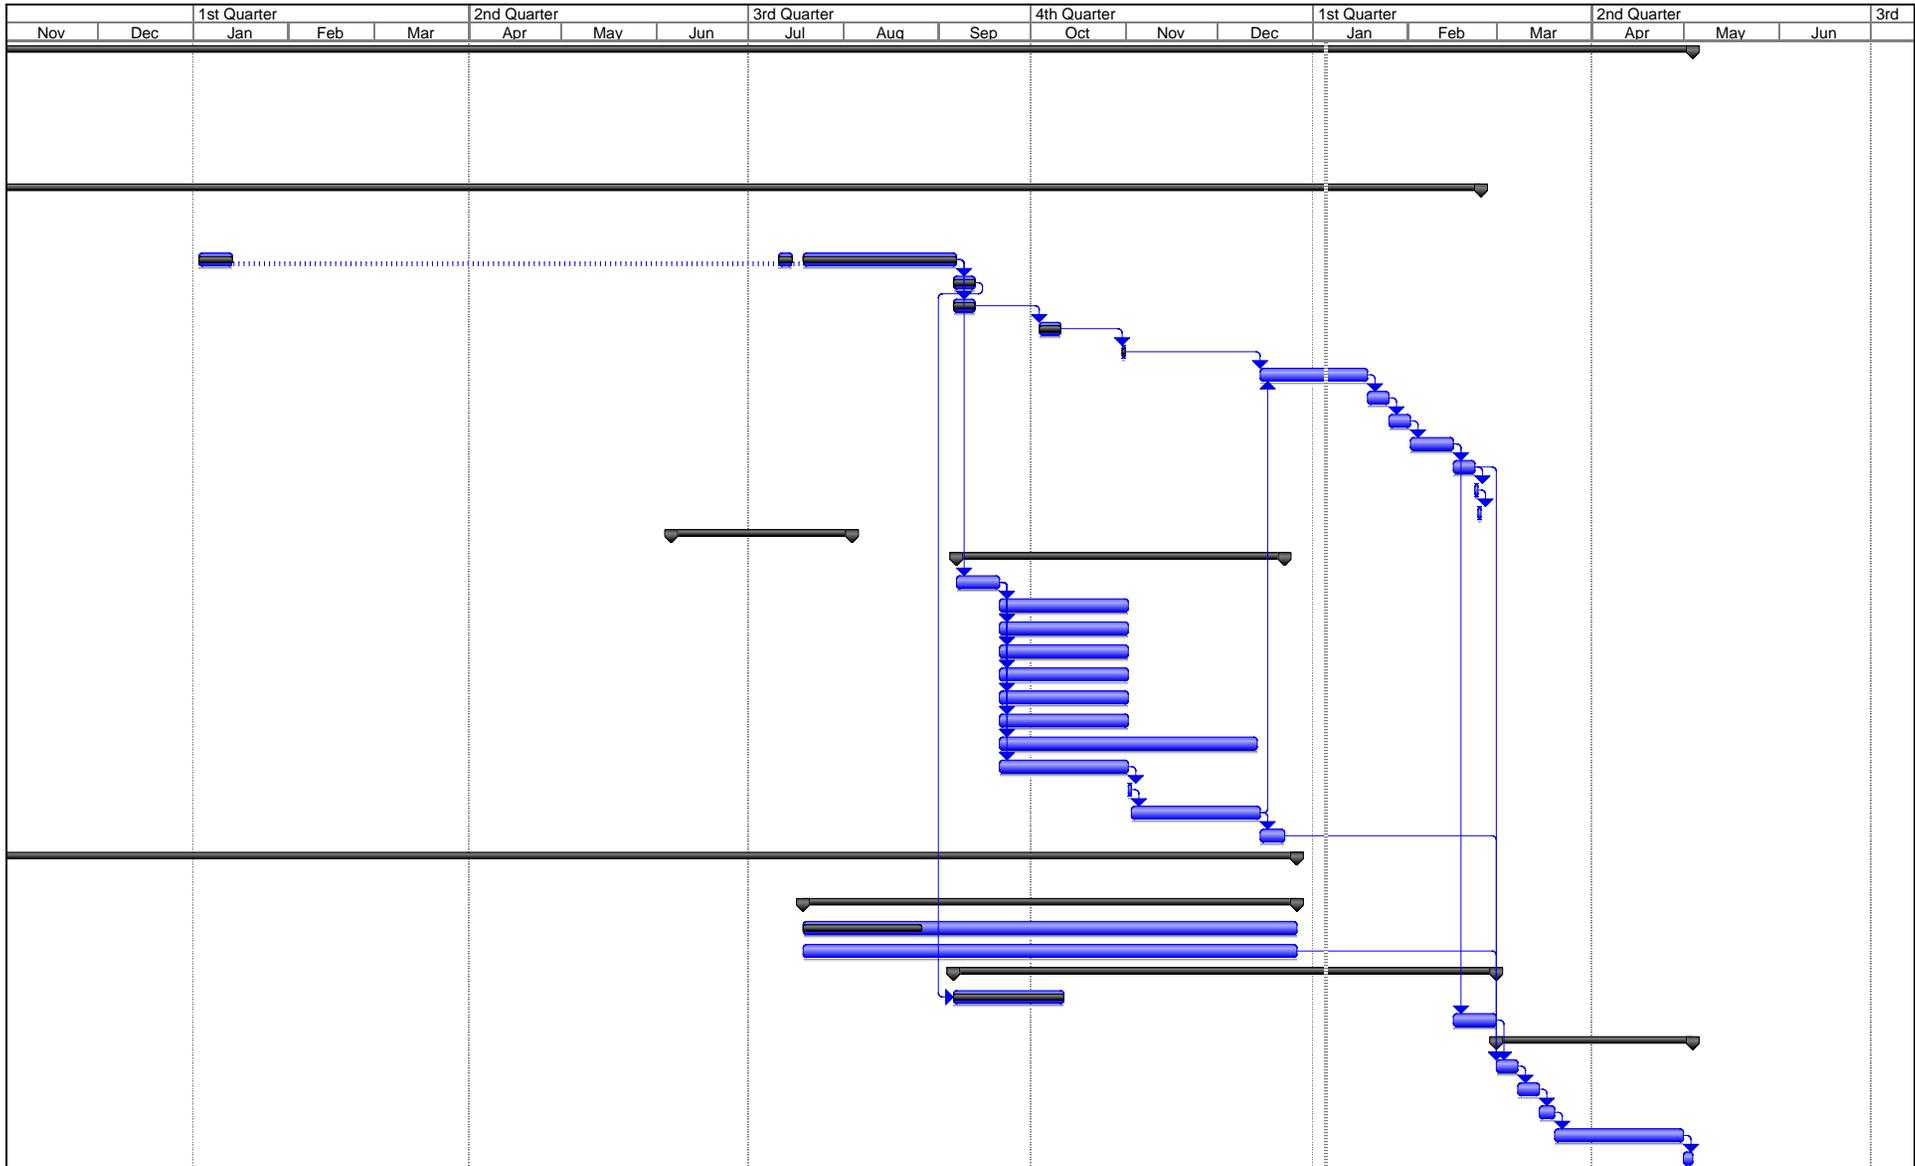

Project: Eek Draft Schedule 0.45mpp  
 Date: Thu 1/5/12

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
