

ID	Task Name	Duration	Start	Finish	Predecessors	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter		
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	
1	Eek Barge Landing	668.25 days	Tue 2/2/10	Fri 8/24/12													
2	Kickoff Meeting	1 day	Tue 2/2/10	Tue 2/2/10													
3	Develop PMP	74 days	Wed 2/3/10	Mon 5/17/10													
11	Site Visit	1 day	Mon 6/21/10	Mon 6/21/10													
12	Trip Report	14 days	Tue 6/22/10	Fri 7/9/10	11												
13	Public Involvement	9 days	Mon 6/21/10	Thu 7/1/10													
15	Engineering and Design	508 days	Tue 6/22/10	Thu 5/31/12													
16	Surveys and Mapping	72 days	Mon 7/12/10	Tue 10/19/10	12,17												
17	Site Development	12 days	Tue 6/22/10	Wed 7/7/10	11												
18	Design	49.5 days	Mon 1/3/11	Tue 9/6/11	32												
19	50% Design for PDT Review	5 days	Tue 9/6/11	Mon 9/12/11	18												
20	50% Design for Chief Review	5 days	Tue 9/6/11	Mon 9/12/11	18												
21	Incorporate Comments	5 days	Tue 10/4/11	Mon 10/10/11	20FS+15 days												
22	Meeting with Customer on Design	1 day	Mon 10/31/11	Mon 10/31/11	21												
23	Plans & Specs	15 days	Wed 4/4/12	Tue 4/24/12	22,45												
24	Plans&Specs, Incorporate Comments	5 days	Wed 4/25/12	Tue 5/1/12	23												
25	Final Design Package for PDT Review	5 days	Wed 5/2/12	Tue 5/8/12	24												
26	Review (ITR)	10 days	Wed 5/9/12	Tue 5/22/12	25												
27	Incorporate Comments	5 days	Wed 5/23/12	Tue 5/29/12	26												
28	PDT Review of Comments Incorporated	1 day	Wed 5/30/12	Wed 5/30/12	27												
29	Final Design Complete	1 day	Thu 5/31/12	Thu 5/31/12	28												
30	Chemical Sampling	43 days	Mon 6/6/11	Wed 8/3/11													
35	Environmental (EA)	146 days	Wed 9/21/11	Wed 4/11/12													
36	Prepare documents	10 days	Wed 2/22/12	Tue 3/6/12	18,32												
37	SHPO	89 days	Wed 9/21/11	Mon 1/23/12	36												
38	F&W Coordination	30 days	Wed 9/21/11	Tue 3/27/12	36												
39	Section 404(b)(1) Analysis	126 days	Wed 9/21/11	Wed 3/14/12	36												
40	Record of Decision	66 days	Wed 9/21/11	Wed 12/21/11	36												
41	Section 103 Evaluation	127 days	Wed 9/21/11	Thu 3/15/12	36												
42	Statement of Findings	66 days	Wed 9/21/11	Wed 12/21/11	36												
43	Draft Final	66 days	Wed 9/21/11	Wed 12/21/11	36												
44	Pre-NEPA Meeting with Customer	1 day	Wed 12/21/11	Wed 12/21/11	43												
45	Public Review	30 days	Wed 2/22/12	Tue 4/3/12	44												
46	Sign FONSI	6 days	Wed 4/4/12	Wed 4/11/12	45												
47	Real Estate	621.25 days	Wed 2/3/10	Thu 6/21/12													
48	Ownership Identification	15 days	Wed 2/3/10	Tue 2/23/10	2												
49	Obtain Permits for Construction	242.25 days	Tue 7/19/11	Thu 6/21/12													
50	From City - Corporation	115 days	Tue 7/19/11	Thu 6/21/12	32												
51	State Tidelands	115 days	Tue 7/19/11	Thu 6/21/12	32												
52	Cost Estimate	196 days	Tue 9/6/11	Tue 6/5/12													
53	50% CWE	26 days	Tue 9/6/11	Tue 10/11/11	19												
54	95% CWE	10 days	Wed 5/23/12	Tue 6/5/12	26												
55	Project Complete	46 days	Thu 6/21/12	Fri 8/24/12													
56	Publication/Reproduction	5 days	Thu 6/21/12	Thu 6/28/12	27,46,51,54												
57	Copies to Customer and Community	5 days	Thu 6/28/12	Thu 7/5/12	56												
58	Physical Closeout	3 days	Thu 7/5/12	Tue 7/10/12	57												
59	Transfer of Remaining Funds	30 days	Tue 7/10/12	Tue 8/21/12	58												
60	Fiscal Closeout	3 days	Tue 8/21/12	Fri 8/24/12	59												

Project: Eek Draft Schedule 0.45mpp
Date: Tue 4/3/12

Task
Split



Progress
Milestone



Summary

Project Summary




External Tasks

External Milestone



Deadline



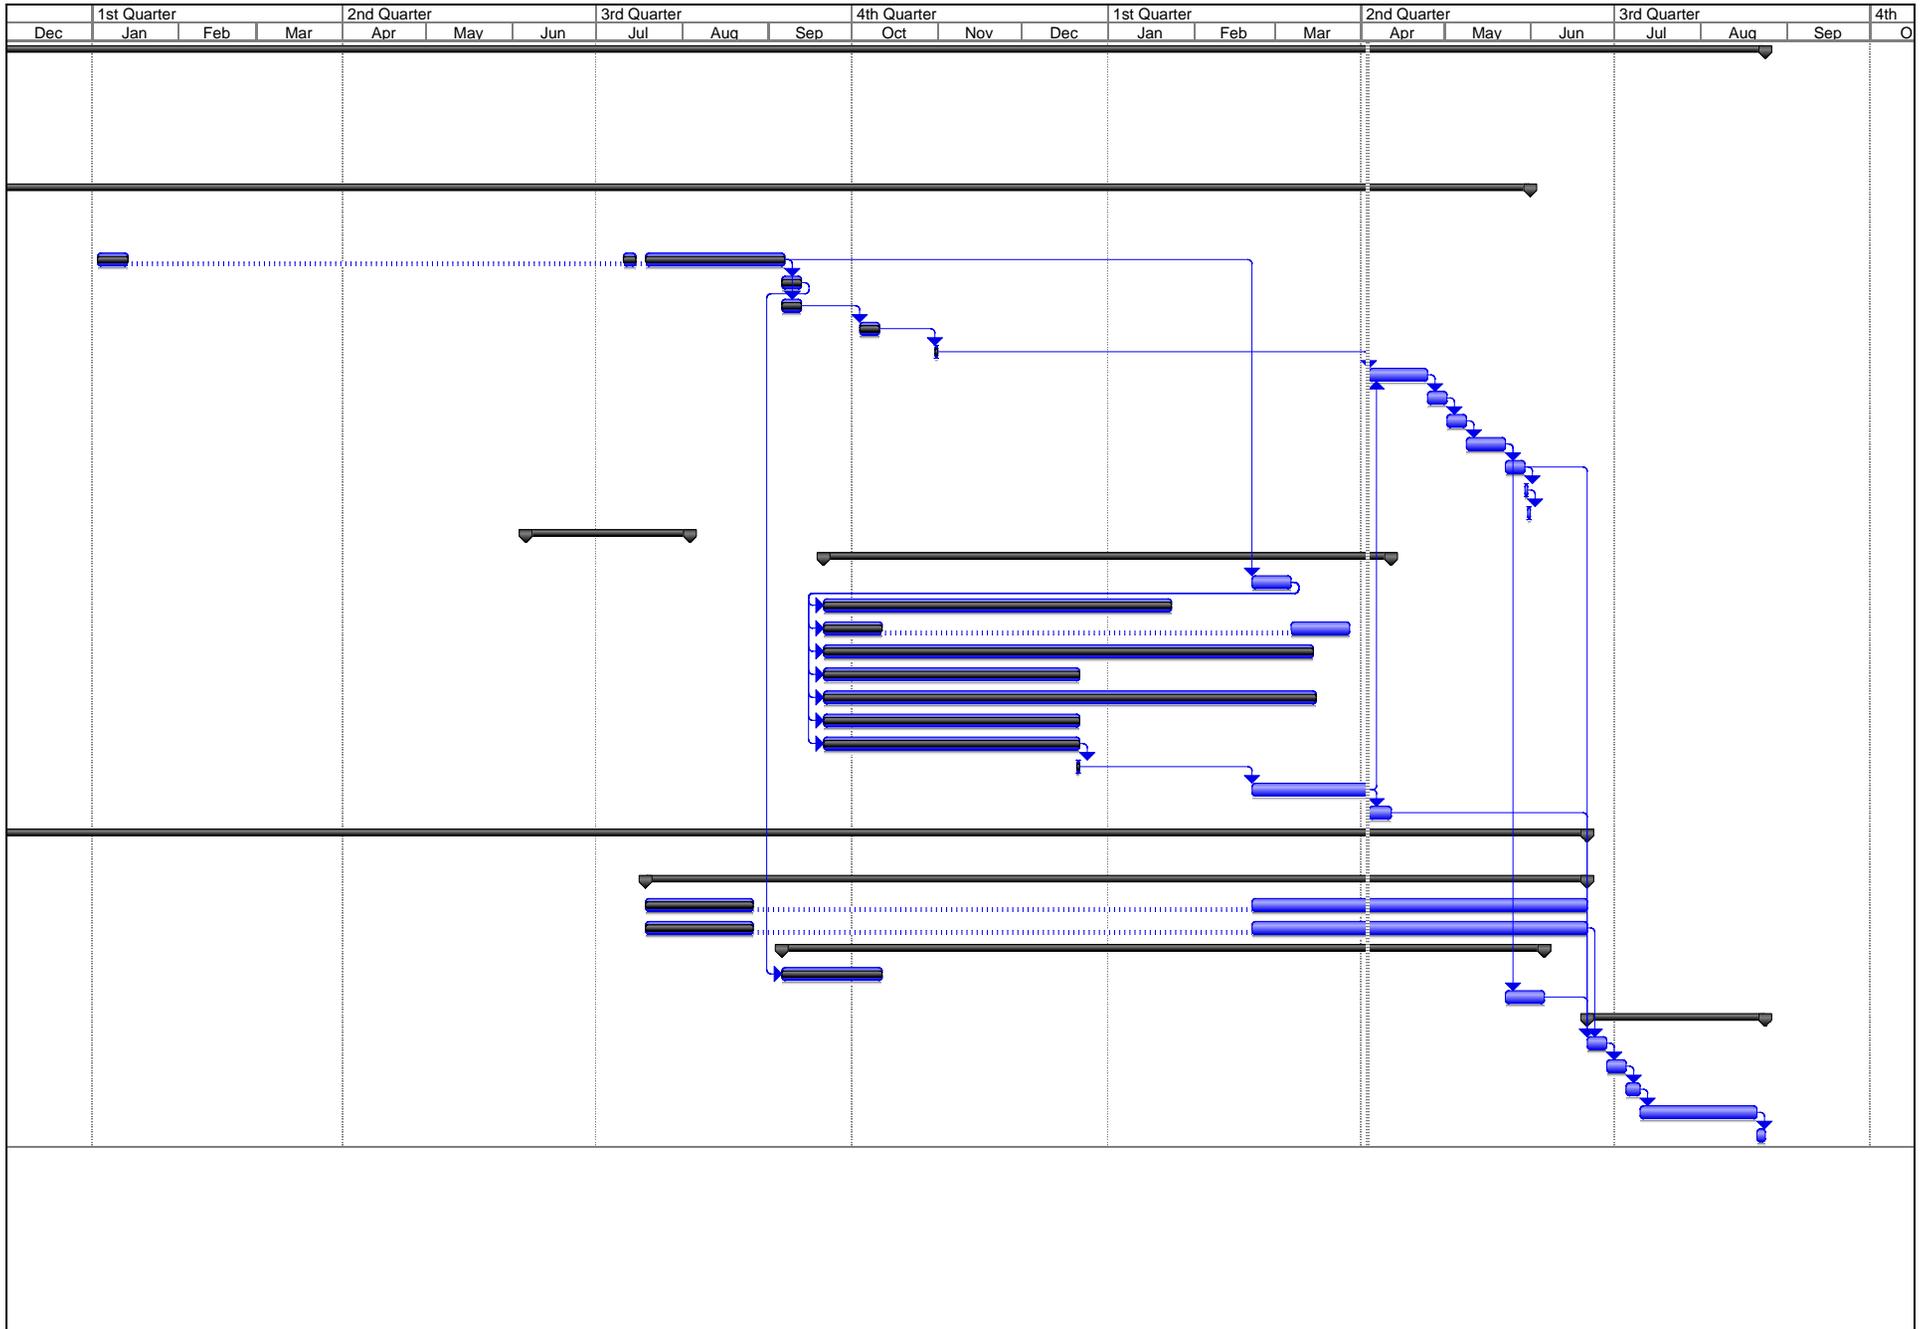

Project: Eek Draft Schedule 0.45mpp Date: Tue 4/3/12	Task		Progress		Summary		External Tasks		Deadline	
	Split		Milestone		Project Summary		External Milestone			
