


ID	Task Name	Duration	Start	Finish	2010											
					3rd Quarter				4th Quarter				1st Quarter			
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
1	Nondalton Barge Landing	618 days?	Thu 7/30/09	Mon 12/12/11												
2	Kickoff Meeting	1 day	Thu 7/30/09	Thu 7/30/09												
3	Develop PMP	93 days	Tue 3/2/10	Thu 7/8/10												
11	Site Visit	1 day	Fri 9/18/09	Fri 9/18/09												
12	Trip Report	10 days	Mon 9/21/09	Fri 10/2/09												
13	Public Involvement	120 days	Mon 10/5/09	Fri 3/19/10												
15	Engineering and Design	522 days?	Sat 10/3/09	Tue 10/4/11												
16	Surveys and Mapping	77 days	Wed 6/23/10	Thu 10/7/10												
17	Site Development	188 days	Sat 10/3/09	Wed 6/23/10												
18	Hydro & Hydraulics	15 days	Mon 1/10/11	Fri 1/28/11												
19	Eng & Design Analysis	30 days	Mon 1/10/11	Fri 2/18/11												
20	Draft Design	3 days	Mon 2/21/11	Wed 2/23/11												
21	Review by PDT	5 days	Thu 2/24/11	Wed 3/2/11												
22	Prepare 50% Draft for Section Chief Review	3 days	Thu 3/3/11	Mon 3/7/11												
23	Review by Section Chiefs	14 days	Tue 3/8/11	Fri 3/25/11												
24	Discussion of 50% with Denali Commission & Nondalton	1 day?	Mon 3/28/11	Mon 3/28/11												
25	Plans&Specs	7 days	Mon 3/28/11	Tue 4/5/11												
26	Review (ITR)	14 days	Thu 9/8/11	Tue 9/27/11												
27	Incorporate Comments	5 days	Wed 9/28/11	Tue 10/4/11												
28	Environmental (EA)	176 days?	Mon 1/10/11	Mon 9/12/11												
29	SHPO	30 days	Mon 1/10/11	Fri 2/18/11												
30	F&W Coordination	30 days	Mon 1/10/11	Fri 2/18/11												
31	Section 404(b)(1) Analysis	30 days	Mon 1/10/11	Fri 2/18/11												
32	Record of Decision	30 days	Mon 1/10/11	Fri 2/18/11												
33	Section 103 Evaluation	30 days	Mon 1/10/11	Fri 2/18/11												
34	Statement of Findings	30 days	Mon 1/10/11	Fri 2/18/11												
35	CZM Consistency	60 days	Mon 1/10/11	Fri 4/1/11												
36	Draft Final	80 days	Mon 4/4/11	Fri 7/22/11												
37	Review with Customer	1 day?	Mon 7/25/11	Mon 7/25/11												
38	Public Review	30 days	Mon 7/25/11	Fri 9/2/11												
39	Final EA	3 days	Mon 9/5/11	Wed 9/7/11												
40	Signed EA	3 days	Thu 9/8/11	Mon 9/12/11												
41	Real Estate	461 days	Fri 7/31/09	Fri 5/6/11												
42	Ownership Identification	186 days	Fri 7/31/09	Sat 4/17/10												
43	Obtain Permits for Construction	227 days	Thu 6/24/10	Fri 5/6/11												
44	From City	135 days	Thu 6/24/10	Fri 5/6/11												
45	State Tidelands	135 days	Thu 6/24/10	Fri 5/6/11												
46	Cost Estimate	45 days	Thu 2/24/11	Wed 4/27/11												

Project: Nondalton Draft Schedule 0.1: Date: Thu 12/16/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	2010									
					3rd Quarter			4th Quarter			1st Quarter			
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
47	Develop Construction Cost	45 days	Thu 2/24/11	Wed 4/27/11										
48	BCOE (Biddibility Constructability Operability Env) R	24 days	Thu 9/8/11	Tue 10/11/11										
49	Review	14 days	Thu 9/8/11	Tue 9/27/11										
50	Incorporate Comments	7 days	Wed 9/28/11	Thu 10/6/11										
51	Certificate	3 days	Fri 10/7/11	Tue 10/11/11										
52	Project Complete	44 days	Wed 10/12/11	Mon 12/12/11										
53	Publication/Reproduction	3 days	Wed 10/12/11	Fri 10/14/11										
54	Copies to Customer and Community	5 days	Mon 10/17/11	Fri 10/21/11										
55	Physical Closeout	3 days	Mon 10/24/11	Wed 10/26/11										
56	Transfer of Remaining Funds	30 days	Thu 10/27/11	Wed 12/7/11										
57	Fiscal Closeout	3 days	Thu 12/8/11	Mon 12/12/11										




Project: Nondalton Draft Schedule 0.1: Date: Thu 12/16/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

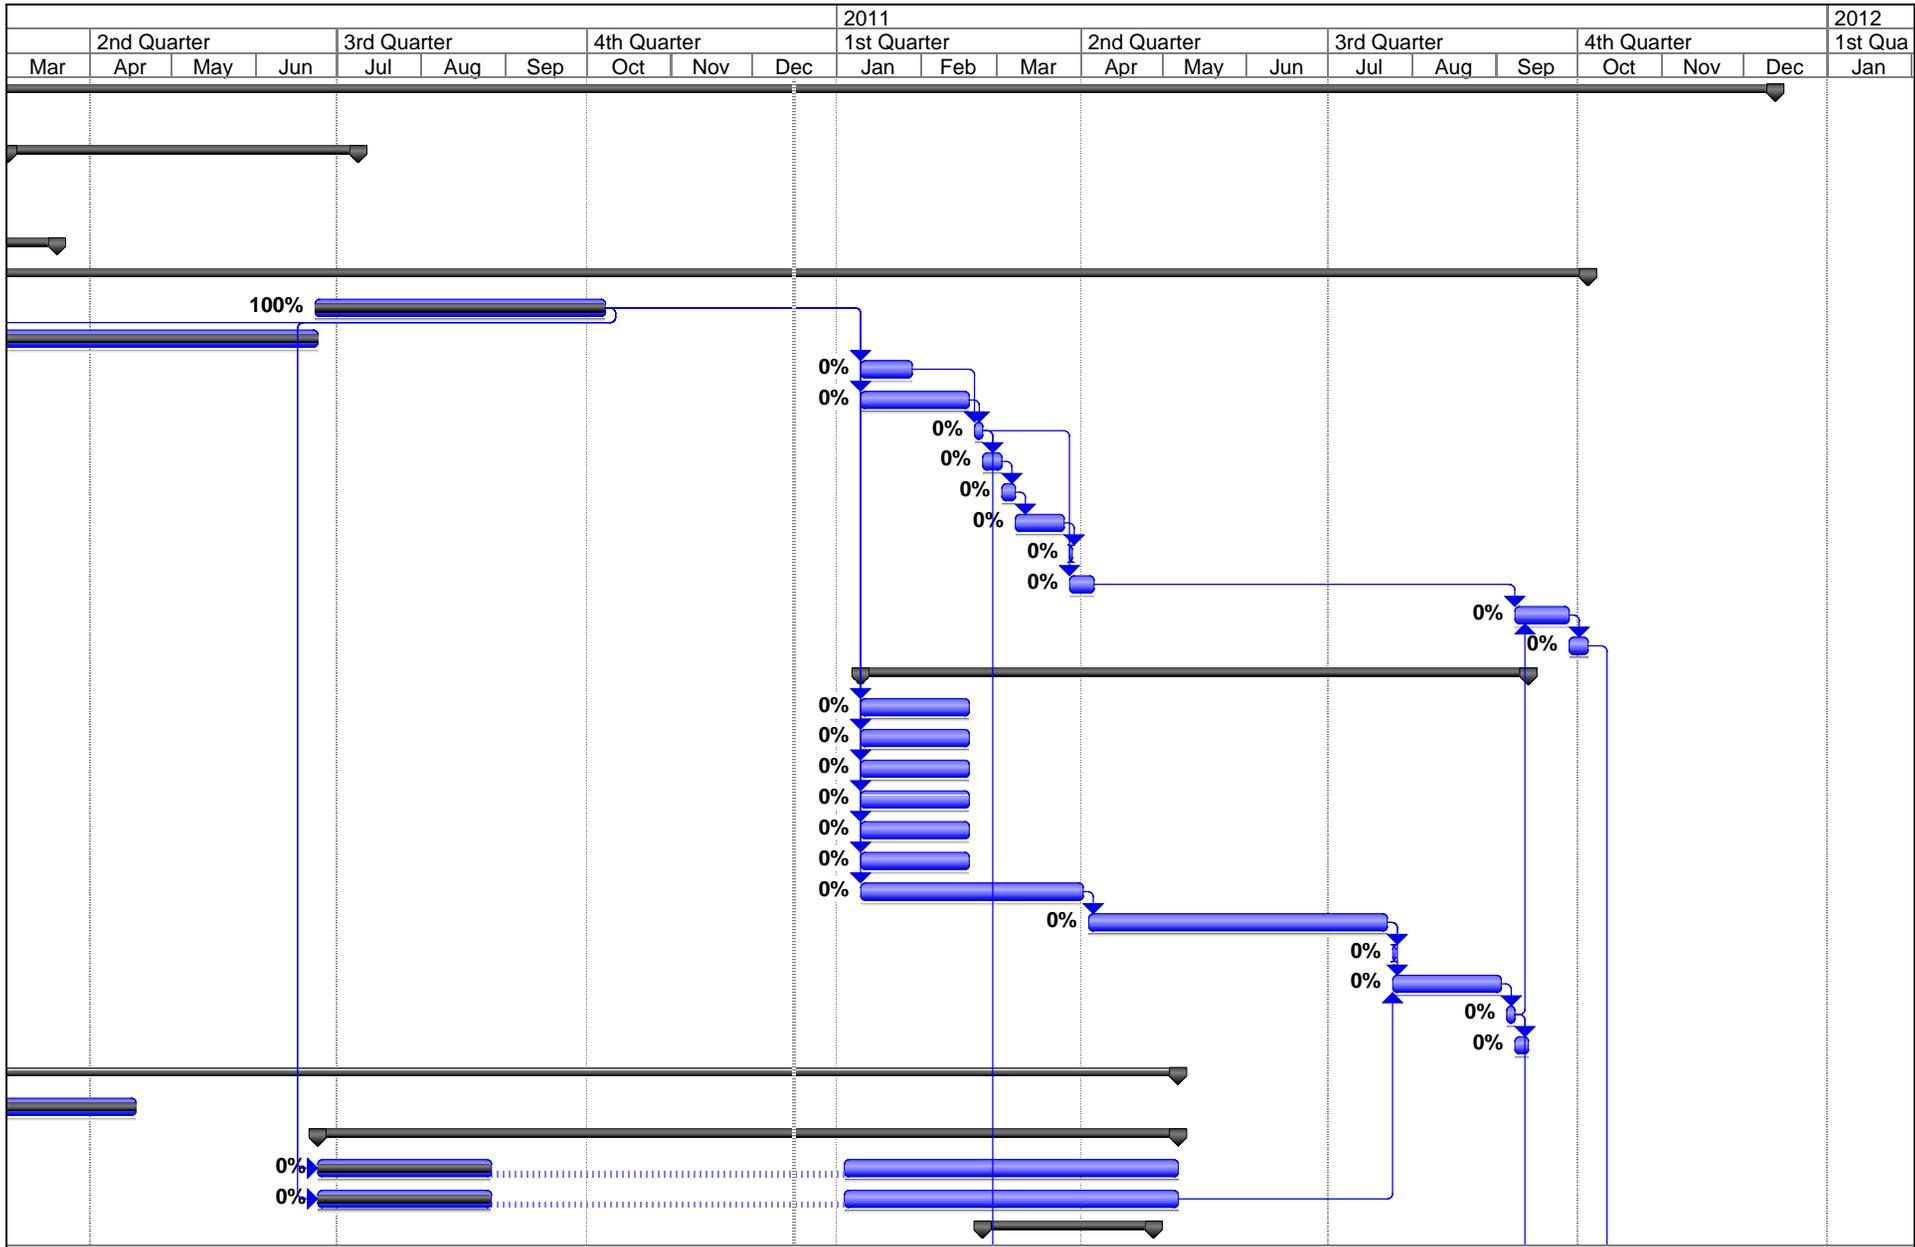

Project: Nondalton Draft Schedule 0.1:
Date: Thu 12/16/10

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

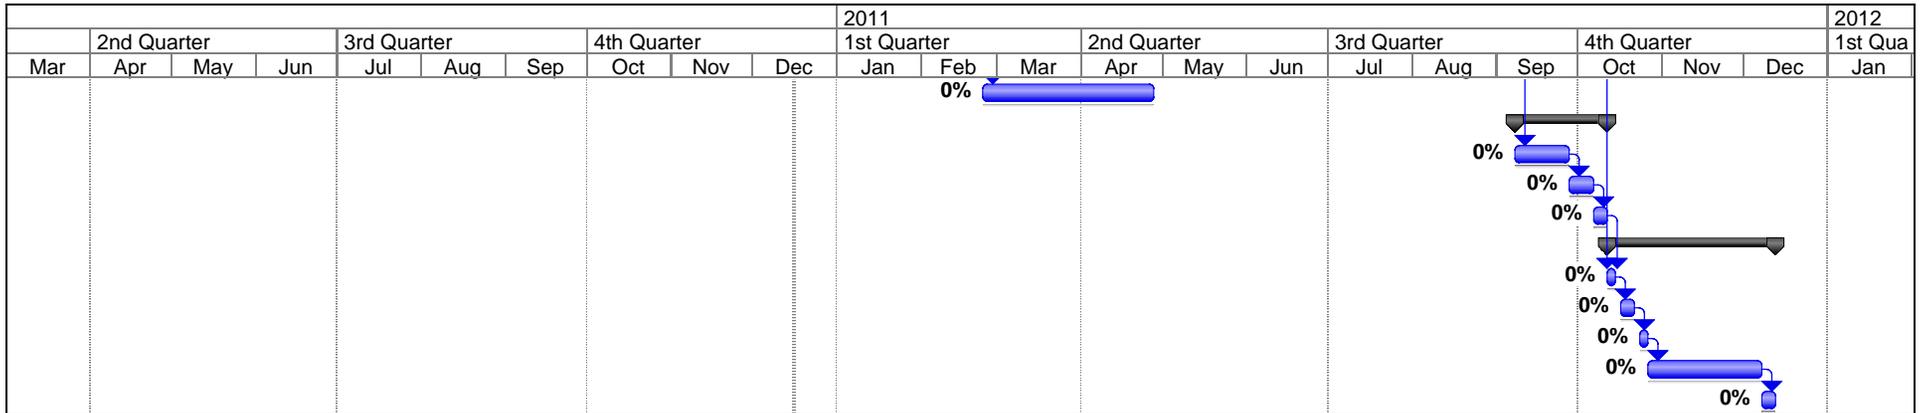

Project: Nondalton Draft Schedule 0.1: Date: Thu 12/16/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
