

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter			4th Quarter			1st Quarter	
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
1	Perryville Barge Landing and Launch Ramp Desi	534 days	Thu 2/17/11	Tue 3/5/13													
2	Kickoff Meeting	1 day	Thu 2/17/11	Thu 2/17/11													
3	Develop PMP	55 days	Wed 2/23/11	Tue 5/10/11													
4	Draft PMP	30 days	Wed 2/23/11	Tue 4/5/11	2												
5	Develop Schedule	8.5 days	Wed 2/23/11	Wed 4/6/11	4												
6	Develop Budget	0.5 days	Wed 2/23/11	Tue 4/5/11	4												
7	PDT Review PMP	29 days	Thu 2/24/11	Tue 4/5/11	5,6												
8	Customer Review of PMP	10 days	Wed 4/6/11	Tue 4/19/11	7												
9	Finalize PMP	10 days	Wed 4/20/11	Tue 5/3/11	8												
10	Approved PMP	5 days	Wed 5/4/11	Tue 5/10/11	9												
11	Site Visit	3 days	Mon 4/11/11	Wed 4/13/11													
12	Trip Report	10 days	Thu 4/14/11	Wed 4/27/11	11												
13	Public Involvement	90 days	Thu 4/14/11	Wed 8/17/11													
14	Community Resolutions	90 days	Thu 4/14/11	Wed 8/17/11	11												
15	Engineering and Design	122.5 days	Thu 3/31/11	Mon 9/19/11													
16	Concept Design	10 days	Thu 4/14/11	Wed 4/27/11	11												
17	Site Development	15 days	Thu 4/28/11	Wed 5/18/11	16												
18	FAA Coordination and Acceptance of Plan	20 days	Thu 3/31/11	Thu 6/9/11	17												
19	Design	20 days	Thu 6/9/11	Thu 7/7/11	18												
20	50% Design for PDT Review	5 days	Thu 7/7/11	Thu 7/14/11	19												
21	50% Design for Chief Review	5 days	Thu 7/14/11	Thu 7/21/11	20												
22	Incorporate Comments	5 days	Thu 7/21/11	Thu 7/28/11	21												
23	Meeting with Customer on Design	1 day	Thu 7/28/11	Fri 7/29/11	22												
24	Plans & Specs	10 days	Fri 7/29/11	Fri 8/12/11	23												
25	Plans&Specs, Incorporate Comments	5 days	Fri 8/12/11	Fri 8/19/11	24												
26	Final Design Package for PDT Review	5 days	Fri 8/19/11	Fri 8/26/11	25												
27	Review (ITR)	10 days	Fri 8/26/11	Fri 9/9/11	26												
28	Incorporate Comments	5 days	Fri 9/9/11	Fri 9/16/11	27												
29	Final Design Complete	1 day	Fri 9/16/11	Mon 9/19/11	28												
30	Environmental (EA)	112 days	Thu 4/28/11	Fri 9/30/11													
31	Prepare documents	15 days	Thu 4/28/11	Wed 5/18/11	12												
32	SHPO	30 days	Thu 5/19/11	Wed 6/29/11	31												
33	F&W Coordination	30 days	Thu 5/19/11	Wed 6/29/11	43,31												
34	Section 404(b)(1) Analysis	30 days	Thu 5/19/11	Wed 6/29/11	31												
35	Record of Decision	30 days	Thu 5/19/11	Wed 6/29/11	31												
36	Statement of Findings	30 days	Thu 5/19/11	Wed 6/29/11	31												
37	CZM Consistency	60 days	Thu 5/19/11	Wed 8/10/11	43,31												
38	Draft Final	60 days	Thu 5/19/11	Wed 8/10/11	31												
39	Pre-NEPA Meeting with Customer	1 day	Thu 8/11/11	Thu 8/11/11	38												
40	Public Review	30 days	Fri 8/12/11	Thu 9/22/11	43,39												

Project: Perryville Design Schedule
Date: Thu 4/7/11

Task  Progress  Summary  External Tasks  Deadline 


Split  Milestone  Project Summary  External Milestone 

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter			4th Quarter			1st Quarter	
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
41	Sign FONSI	6 days	Fri 9/23/11	Fri 9/30/11	40												
42	Real Estate	180 days	Thu 2/24/11	Wed 11/2/11													
43	Ownership Identification	10 days	Thu 2/24/11	Wed 3/9/11													
44	Obtain Permits for Construction	120 days	Thu 5/19/11	Wed 11/2/11													
45	From City/Tribe/Corporation	120 days	Thu 5/19/11	Wed 11/2/11	17												
46	State Tidelands Permits - Lease	120 days	Thu 5/19/11	Wed 11/2/11	17												
47	Cost Estimate	67 days	Thu 7/7/11	Mon 10/10/11													
48	35% Estimate	10 days	Thu 7/7/11	Thu 7/21/11	19												
49	95% Estiamte	10 days	Mon 9/19/11	Mon 10/3/11	29												
50	IGE	5 days	Mon 10/3/11	Mon 10/10/11	49												
51	BCOE Review	18 days	Mon 10/3/11	Wed 10/26/11													
52	Review	10 days	Mon 10/3/11	Fri 10/14/11	29,41,35												
53	Incorporate Comments	5 days	Mon 10/17/11	Fri 10/21/11	52												
54	Certificate	3 days	Mon 10/24/11	Wed 10/26/11	53												
55	Contracting - CW IDIQ	41 days	Thu 10/27/11	Thu 12/22/11													
56	Prepare Solication Letter and Package	5 days	Thu 10/27/11	Wed 11/2/11	54												
57	RFP	10 days	Thu 11/3/11	Wed 11/16/11	56												
58	Negotiation	10 days	Thu 11/17/11	Wed 11/30/11	57												
59	Award	5 days	Thu 12/1/11	Wed 12/7/11	58												
60	Bond	10 days	Thu 12/8/11	Wed 12/21/11	59												
61	NTP	1 day	Thu 12/22/11	Thu 12/22/11	60												
62	Construction	276 days	Fri 12/23/11	Fri 1/11/13													
63	Pre-construction Conference	1 day	Fri 12/23/11	Fri 12/23/11	61												
64	Construction	260 days	Mon 12/26/11	Fri 12/21/12	63												
65	Final Inspection	1 day	Mon 12/24/12	Mon 12/24/12	64												
66	Project closeout	14 days	Tue 12/25/12	Fri 1/11/13	65												
67	Project Complete	37 days	Mon 1/14/13	Tue 3/5/13													
68	Physical Closeout	3 days	Mon 1/14/13	Wed 1/16/13	66												
69	Transfer of Remaining Funds	30 days	Thu 1/17/13	Wed 2/27/13	68												
70	Fiscal Closeout	3 days	Thu 2/28/13	Mon 3/4/13	69												
71	Project Closed Out	1 day	Tue 3/5/13	Tue 3/5/13	70												

Project: Perryville Design Schedule
Date: Thu 4/7/11

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

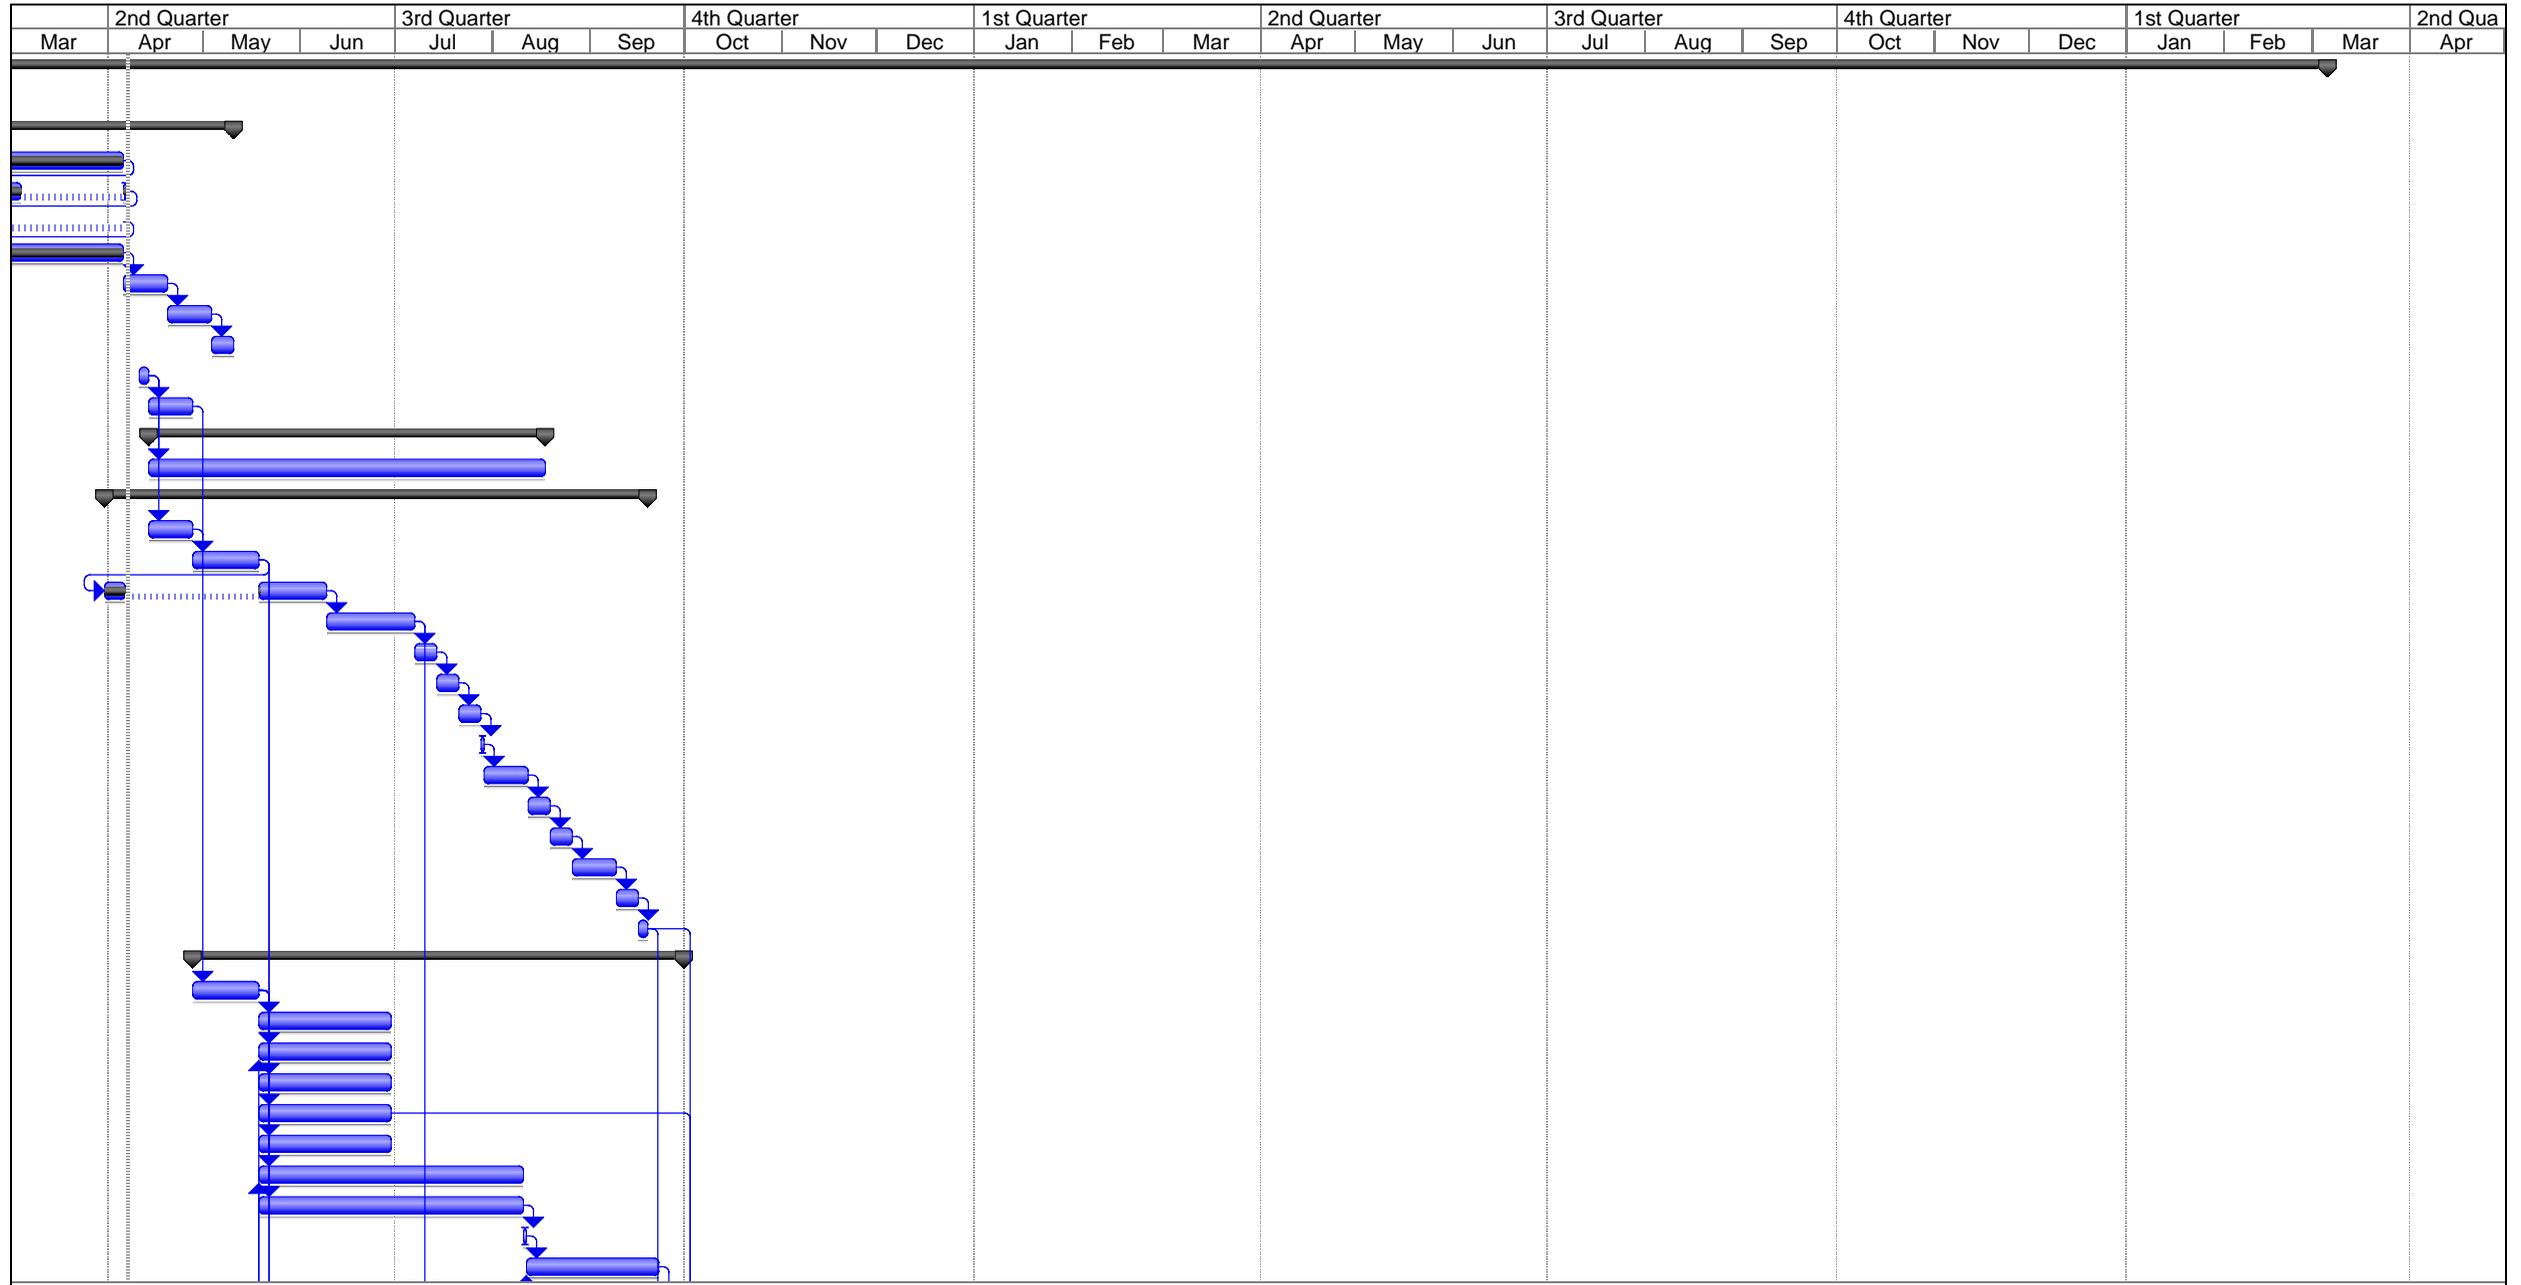

Project: Perryville Design Schedule
Date: Thu 4/7/11


Task 
Split 

Progress 
Milestone 

Summary 
Project Summary 

External Tasks 
External Milestone 

Deadline 

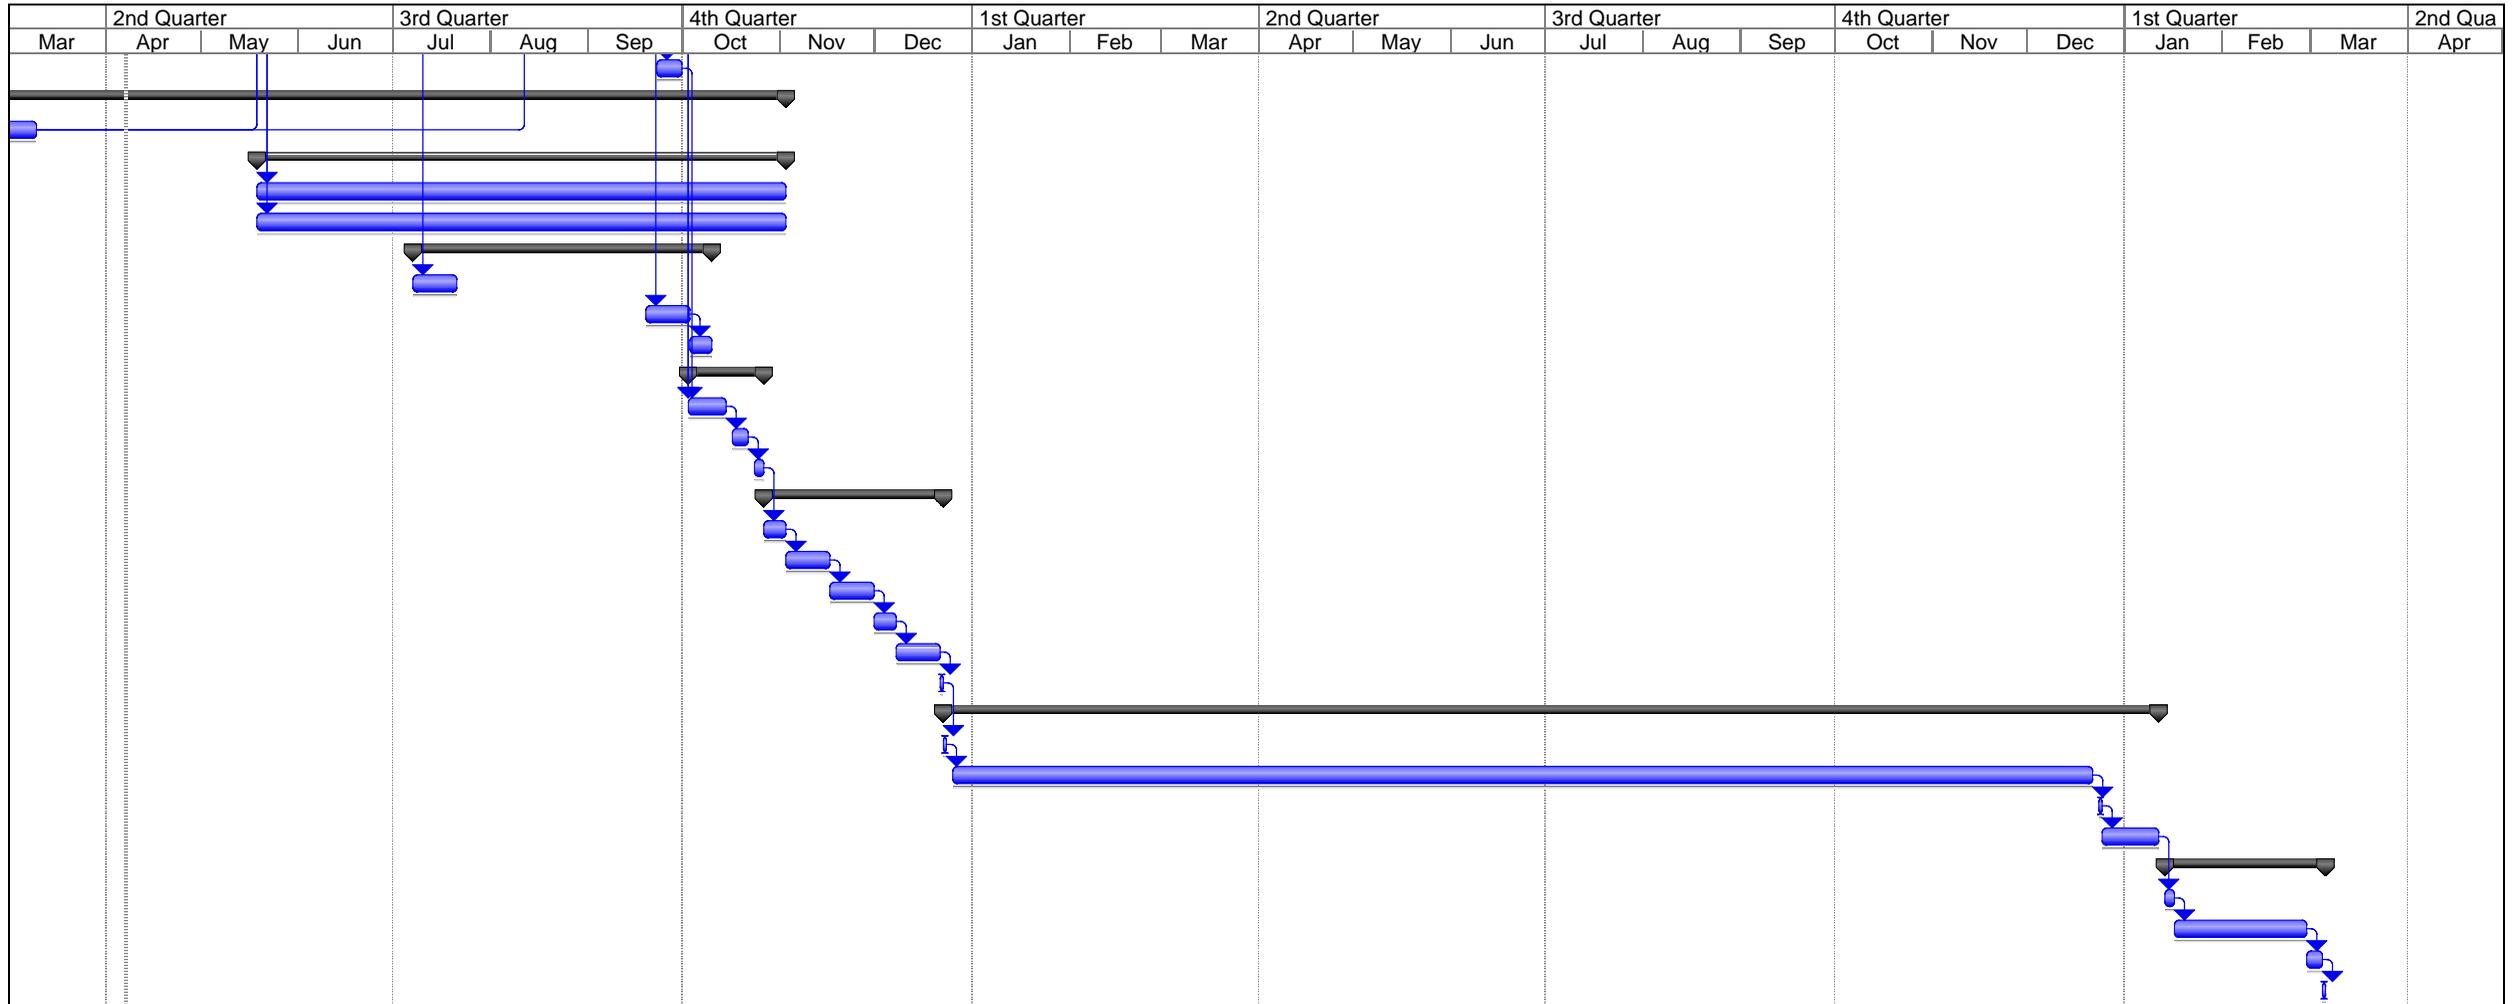

Project: Perryville Design Schedule
Date: Thu 4/7/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
