


ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter			4th Quarter			1st Quarter		
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
1	Perryville Barge Landing and Launch Ramp Desi	571 days	Thu 2/17/11	Thu 4/25/13														
2	Kickoff Meeting	1 day	Thu 2/17/11	Thu 2/17/11														
3	Develop PMP	55 days	Wed 2/23/11	Tue 5/10/11														
11	Site Visit	3 days	Mon 4/11/11	Wed 4/13/11														
12	Trip Report	18 days	Thu 4/14/11	Mon 5/9/11	11													
13	Public Involvement	90 days	Thu 4/14/11	Wed 8/17/11														
14	Community Resolutions	90 days	Thu 4/14/11	Wed 8/17/11	11													
15	Engineering and Design	169 days	Thu 3/31/11	Tue 11/22/11														
16	Concept Design	10 days	Thu 4/14/11	Wed 4/27/11	11													
17	Site Development	15 days	Thu 4/28/11	Wed 5/18/11	16													
18	FAA Coordination and Acceptance of Plan	28.5 days	Thu 3/31/11	Tue 7/12/11	17													
19	Design	19 days	Wed 7/13/11	Mon 8/8/11	18													
20	50% Design for PDT Review	14 days	Tue 8/9/11	Fri 8/26/11	19													
21	50% Design for Chief Review	20 days	Mon 8/29/11	Fri 9/23/11	20													
22	Incorporate Comments	5 days	Mon 9/26/11	Fri 9/30/11	21													
23	Meeting with Customer on Design	1 day	Mon 10/3/11	Mon 10/3/11	22													
24	Plans & Specs	10 days	Tue 10/4/11	Mon 10/17/11	23													
25	Plans&Specs, Incorporate Comments	5 days	Tue 10/18/11	Mon 10/24/11	24													
26	Final Design Package for PDT Review	5 days	Tue 10/25/11	Mon 10/31/11	25													
27	Review (ITR)	10 days	Tue 11/1/11	Mon 11/14/11	26													
28	Incorporate Comments	5 days	Tue 11/15/11	Mon 11/21/11	27													
29	Final Design Complete	1 day	Tue 11/22/11	Tue 11/22/11	28													
30	Environmental (EA)	112 days	Tue 5/10/11	Wed 10/12/11														
31	Prepare documents	15 days	Tue 5/10/11	Mon 5/30/11	12													
32	SHPO	30 days	Tue 5/31/11	Mon 7/11/11	31													
33	F&W Coordination	30 days	Tue 5/31/11	Mon 7/11/11	43,31													
34	Section 404(b)(1) Analysis	30 days	Tue 5/31/11	Mon 7/11/11	31													
35	Record of Decision	30 days	Tue 5/31/11	Mon 7/11/11	31													
36	Statement of Findings	30 days	Tue 5/31/11	Mon 7/11/11	31													
37	CZM Consistency	60 days	Tue 5/31/11	Mon 8/22/11	43,31													
38	Draft Final	60 days	Tue 5/31/11	Mon 8/22/11	31													
39	Pre-NEPA Meeting with Customer	1 day	Tue 8/23/11	Tue 8/23/11	38													
40	Public Review	30 days	Wed 8/24/11	Tue 10/4/11	43,39													
41	Sign FONSI	6 days	Wed 10/5/11	Wed 10/12/11	40													
42	Real Estate	180 days	Thu 2/24/11	Wed 11/2/11														
43	Ownership Identification	10 days	Thu 2/24/11	Wed 3/9/11														
44	Obtain Permits for Construction	120 days	Thu 5/19/11	Wed 11/2/11														
45	From City/Tribe/Corporation	120 days	Thu 5/19/11	Wed 11/2/11	17													
46	State Tidelands Permits - Lease	120 days	Thu 5/19/11	Wed 11/2/11	17													
47	Cost Estimate	44 days	Tue 8/9/11	Fri 10/7/11														

Project: Perryville Design Schedule
Date: Fri 9/30/11

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone


ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter			4th Quarter			1st Quarter		
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
48	50% Estiamte	39 days	Tue 8/9/11	Fri 9/30/11	19													
49	IGE	5 days	Mon 10/3/11	Fri 10/7/11	48													
50	BCOE Review	18 days	Wed 11/23/11	Fri 12/16/11														
51	Review	10 days	Wed 11/23/11	Tue 12/6/11	29,41,35													
52	Incorporate Comments	5 days	Wed 12/7/11	Tue 12/13/11	51													
53	Certificate	3 days	Wed 12/14/11	Fri 12/16/11	52													
54	Contracting - CW IDIQ	41 days	Mon 12/19/11	Mon 2/13/12														
55	Prepare Solicitation Letter and Package	5 days	Mon 12/19/11	Fri 12/23/11	53													
56	RFP	10 days	Mon 12/26/11	Fri 1/6/12	55													
57	Negotiation	10 days	Mon 1/9/12	Fri 1/20/12	56													
58	Award	5 days	Mon 1/23/12	Fri 1/27/12	57													
59	Bond	10 days	Mon 1/30/12	Fri 2/10/12	58													
60	NTP	1 day	Mon 2/13/12	Mon 2/13/12	59													
61	Construction	276 days	Tue 2/14/12	Tue 3/5/13														
62	Pre-construction Conference	1 day	Tue 2/14/12	Tue 2/14/12	60													
63	Construction	260 days	Wed 2/15/12	Tue 2/12/13	62													
64	Final Inspection	1 day	Wed 2/13/13	Wed 2/13/13	63													
65	Project closeout	14 days	Thu 2/14/13	Tue 3/5/13	64													
66	Project Complete	37 days	Wed 3/6/13	Thu 4/25/13														
67	Physical Closeout	3 days	Wed 3/6/13	Fri 3/8/13	65													
68	Transfer of Remaining Funds	30 days	Mon 3/11/13	Fri 4/19/13	67													
69	Fiscal Closeout	3 days	Mon 4/22/13	Wed 4/24/13	68													
70	Project Closed Out	1 day	Thu 4/25/13	Thu 4/25/13	69													



Project: Perryville Design Schedule
Date: Fri 9/30/11


Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

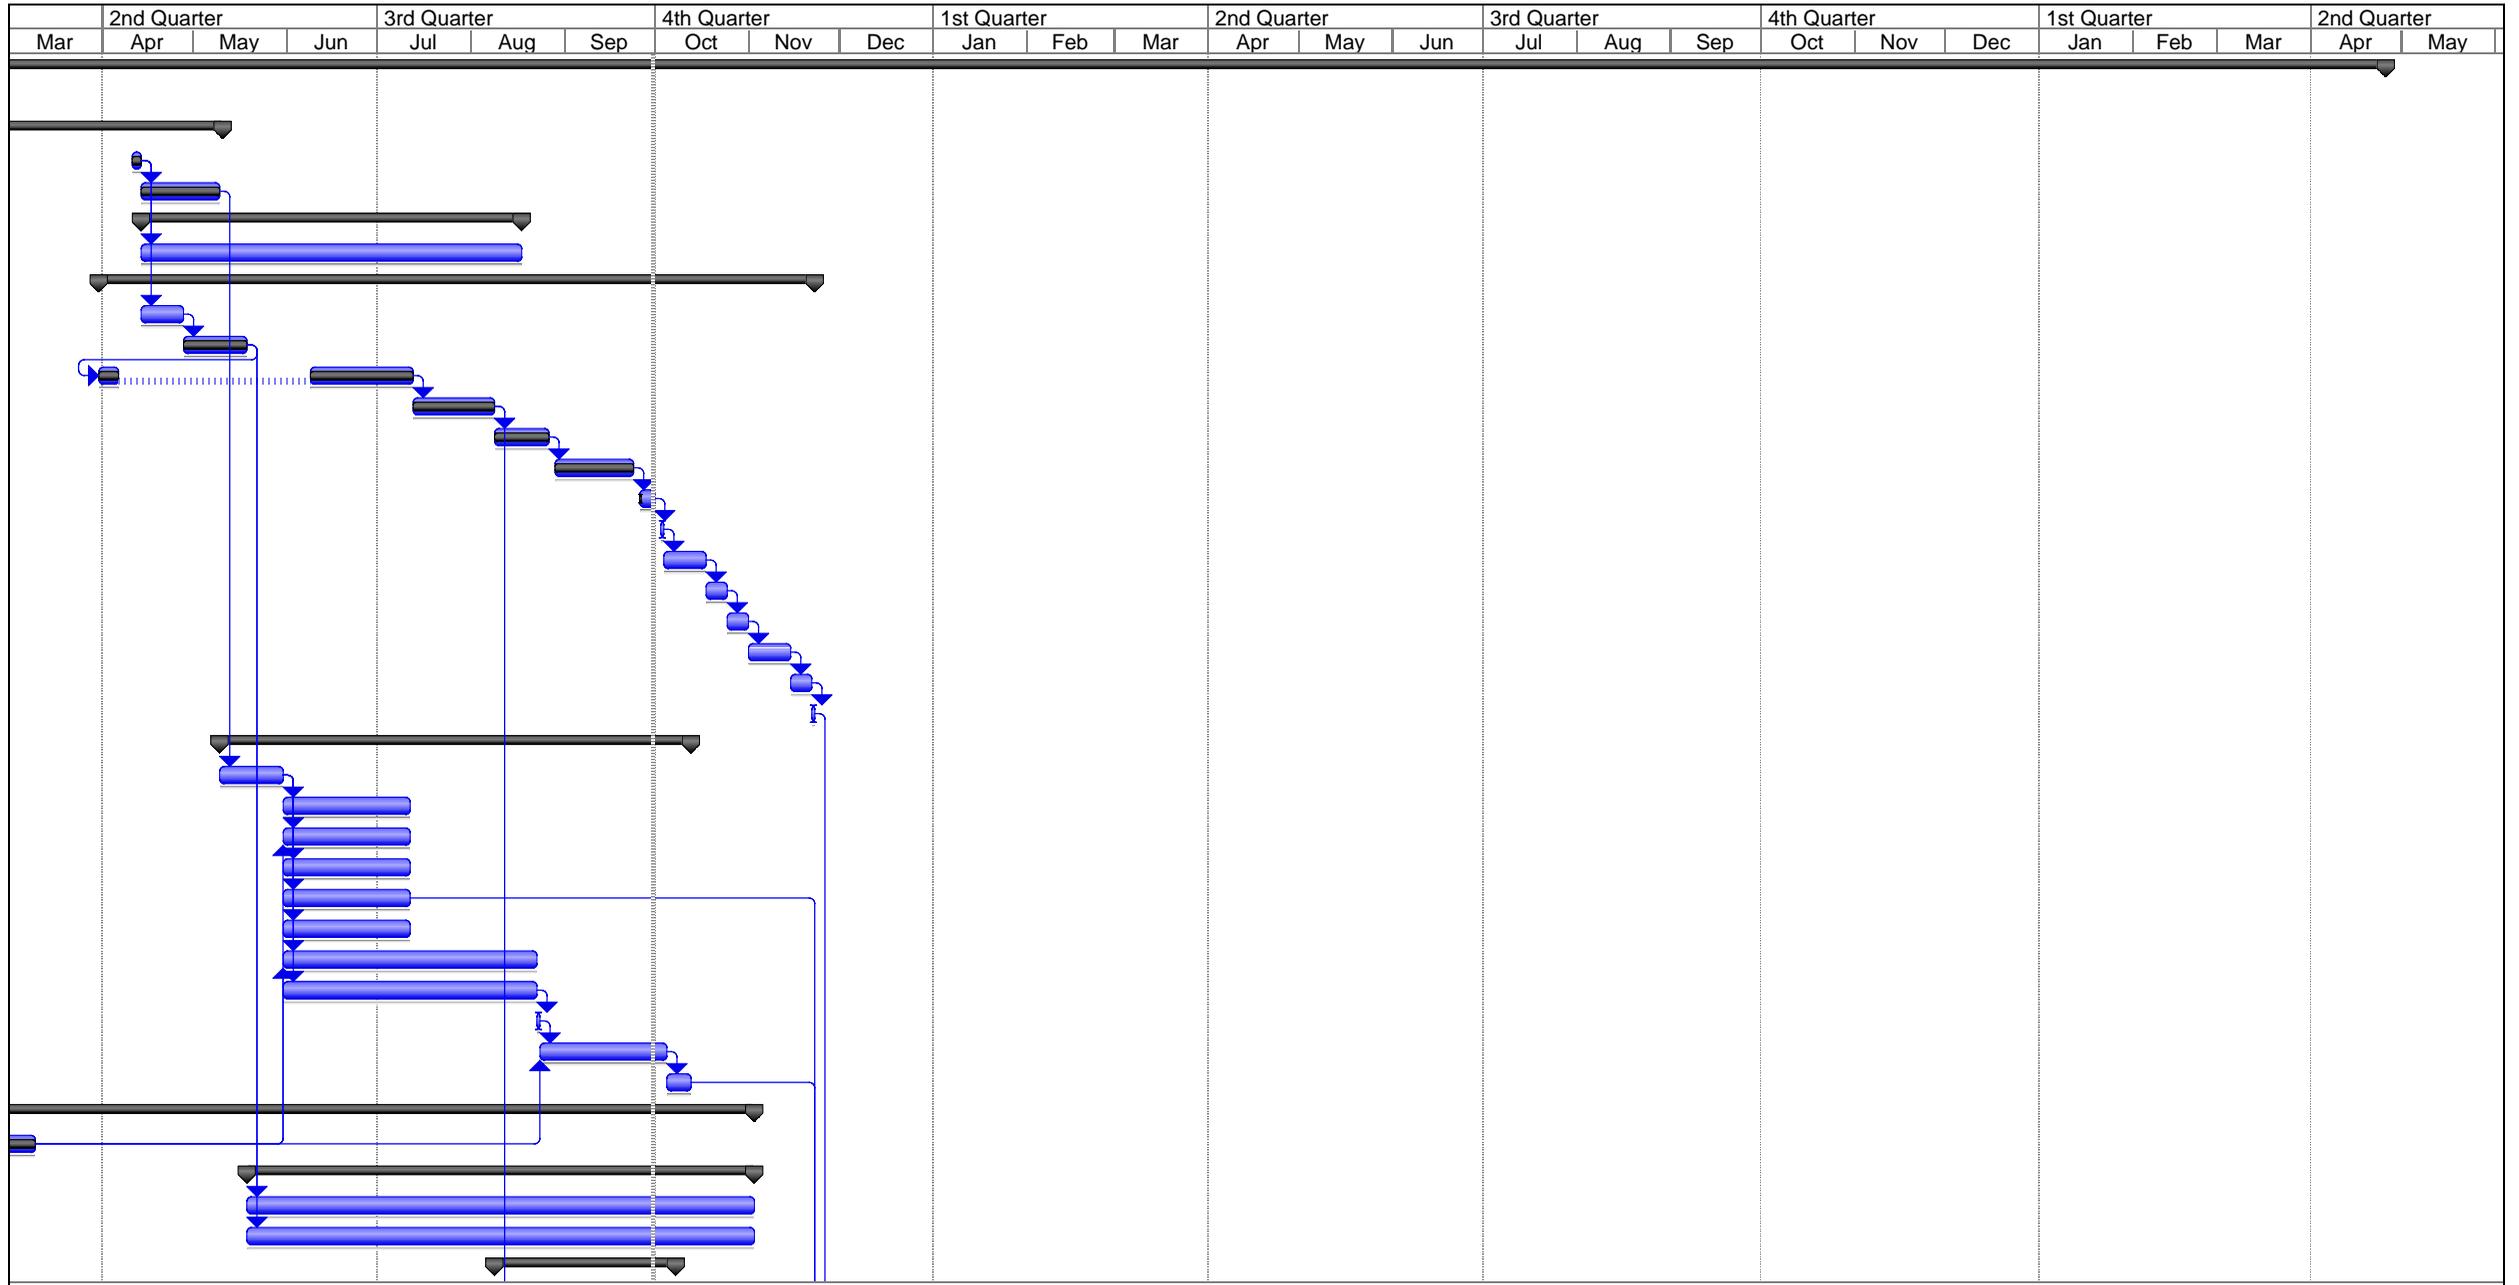

Project: Perryville Design Schedule
 Date: Fri 9/30/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

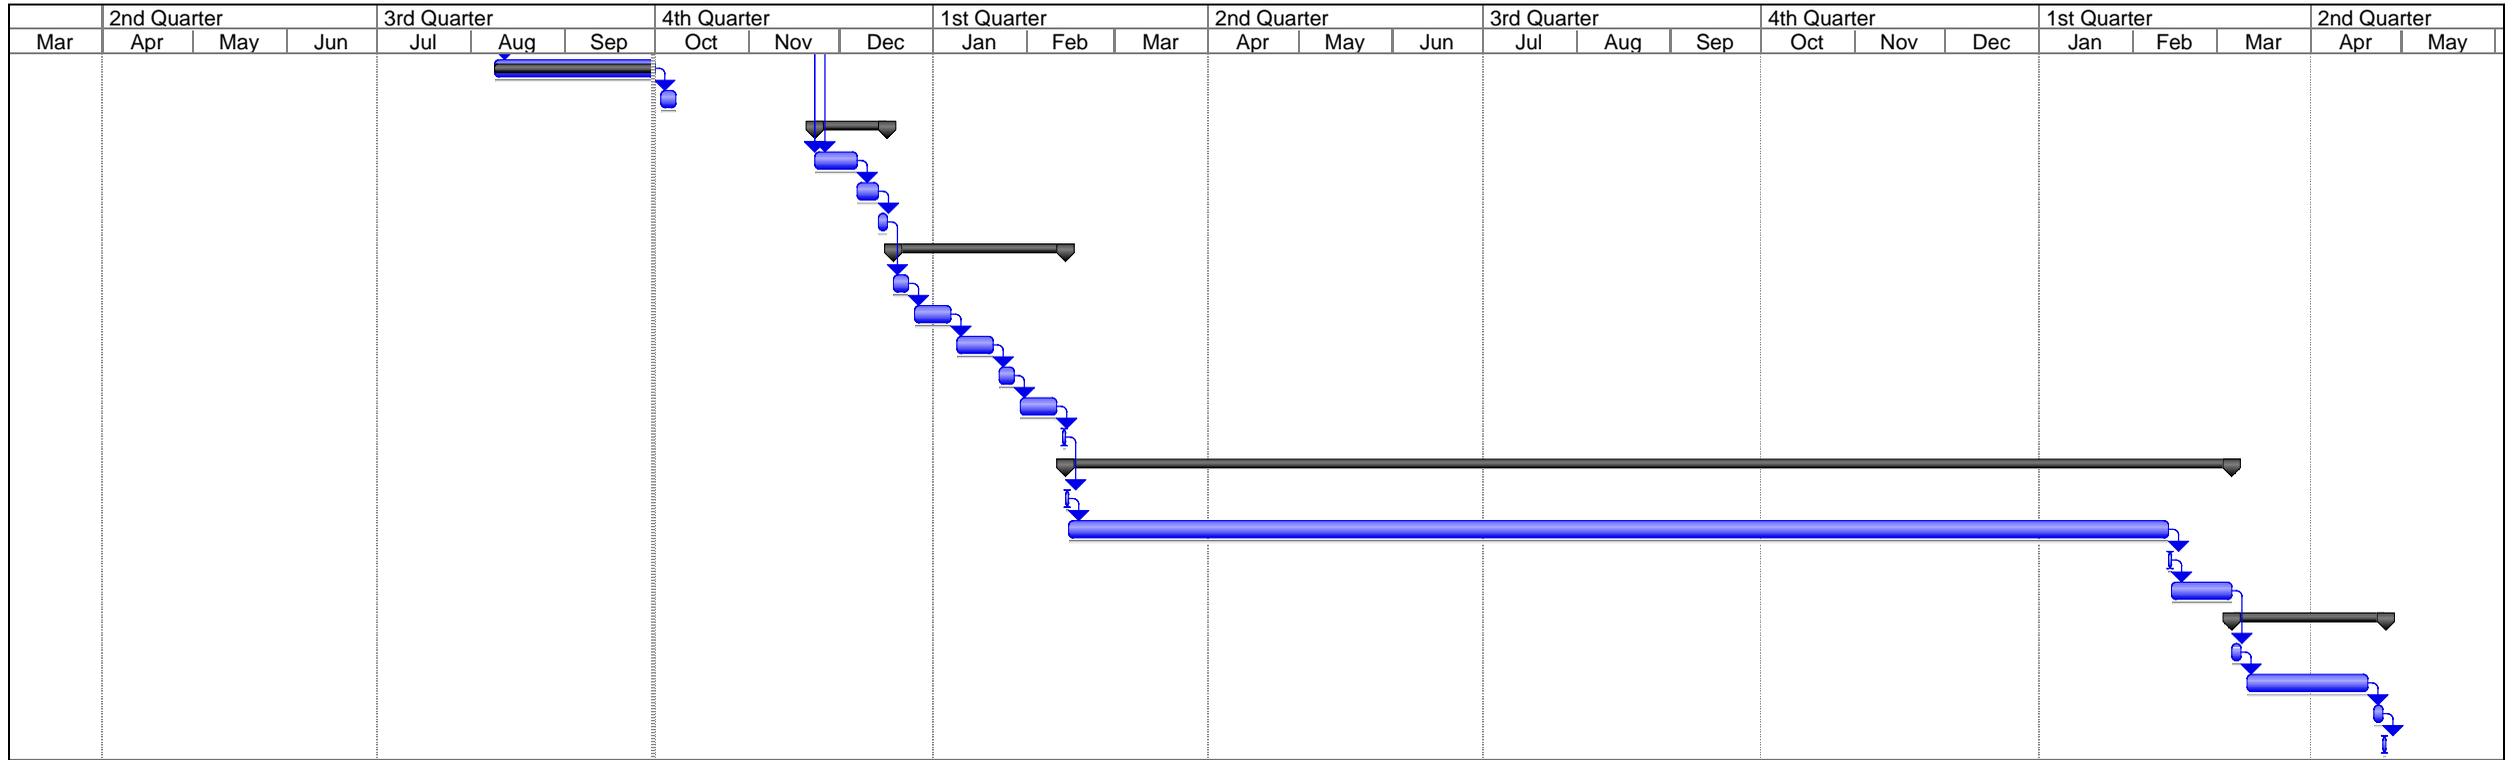

Project: Perryville Design Schedule
 Date: Fri 9/30/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
