

ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter			4th Quarter			1st Quarter			2n
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	
1	Perryville Barge Landing and Launch Ramp Desi	610 days	Thu 2/17/11	Wed 6/19/13															
2	Kickoff Meeting	1 day	Thu 2/17/11	Thu 2/17/11															
3	Develop PMP	55 days	Wed 2/23/11	Tue 5/10/11															
11	Site Visit	3 days	Mon 4/11/11	Wed 4/13/11															
12	Trip Report	18 days	Thu 4/14/11	Mon 5/9/11	11														
13	Public Involvement	90 days	Thu 4/14/11	Wed 8/17/11															
14	Community Resolutions	90 days	Thu 4/14/11	Wed 8/17/11	11														
15	Engineering and Design	208 days	Thu 3/31/11	Mon 1/16/12															
16	Concept Design	10 days	Thu 4/14/11	Wed 4/27/11	11														
17	Site Development	15 days	Thu 4/28/11	Wed 5/18/11	16														
18	FAA Coordination and Acceptance of Plan	28.5 days	Thu 3/31/11	Tue 7/12/11	17														
19	Design	19 days	Wed 7/13/11	Mon 8/8/11	18														
20	50% Design for PDT Review	14 days	Tue 8/9/11	Fri 8/26/11	19														
21	50% Design for Chief Review	20 days	Mon 8/29/11	Fri 9/23/11	20														
22	Incorporate Comments	44 days	Mon 9/26/11	Thu 11/24/11	21														
23	Meeting with Customer on Design	1 day	Fri 11/25/11	Fri 11/25/11	22														
24	Plans & Specs	10 days	Mon 11/28/11	Fri 12/9/11	23,40														
25	Plans&Specs, Incorporate Comments	5 days	Mon 12/12/11	Fri 12/16/11	24														
26	Final Design Package for PDT Review	5 days	Mon 12/19/11	Fri 12/23/11	25														
27	Review (ITR)	10 days	Mon 12/26/11	Fri 1/6/12	26														
28	Incorporate Comments	5 days	Mon 1/9/12	Fri 1/13/12	27														
29	Final Design Complete	1 day	Mon 1/16/12	Mon 1/16/12	28														
30	Environmental (EA)	112 days	Tue 5/10/11	Wed 10/12/11															
31	Prepare documents	15 days	Tue 5/10/11	Mon 5/30/11	12														
32	SHPO	30 days	Tue 5/31/11	Mon 7/11/11	31														
33	F&W Coordination	30 days	Tue 5/31/11	Mon 7/11/11	43,31														
34	Section 404(b)(1) Analysis	30 days	Tue 5/31/11	Mon 7/11/11	31														
35	Record of Decision	30 days	Tue 5/31/11	Mon 7/11/11	31														
36	Statement of Findings	30 days	Tue 5/31/11	Mon 7/11/11	31														
37	CZM Consistency	60 days	Tue 5/31/11	Mon 8/22/11	43,31														
38	Draft Final	60 days	Tue 5/31/11	Mon 8/22/11	31														
39	Pre-NEPA Meeting with Customer	1 day	Tue 8/23/11	Tue 8/23/11	38														
40	Public Review	30 days	Wed 8/24/11	Tue 10/4/11	43,39														
41	Sign FONSI	6 days	Wed 10/5/11	Wed 10/12/11	40														
42	Real Estate	180 days	Thu 2/24/11	Wed 11/2/11															
43	Ownership Identification	10 days	Thu 2/24/11	Wed 3/9/11															
44	Obtain Permits for Construction	120 days	Thu 5/19/11	Wed 11/2/11															
45	From City/Tribe/Corporation	120 days	Thu 5/19/11	Wed 11/2/11	17														
46	State Tidelands Permits - Lease	120 days	Thu 5/19/11	Wed 11/2/11	17														
47	Cost Estimate	44 days	Tue 8/9/11	Fri 10/7/11															

Project: Perryville Design Schedule
Date: Thu 1/5/12

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone


ID	Task Name	Duration	Start	Finish	Predecessors	2nd Quarter				3rd Quarter			4th Quarter			1st Quarter			2n
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	
48	50% Estiamte	39 days	Tue 8/9/11	Fri 9/30/11	19														
49	IGE	5 days	Mon 10/3/11	Fri 10/7/11	48														
50	BCOE Review	18 days	Tue 1/17/12	Thu 2/9/12															
51	Review	10 days	Tue 1/17/12	Mon 1/30/12	29,41,35														
52	Incorporate Comments	5 days	Tue 1/31/12	Mon 2/6/12	51														
53	Certificate	3 days	Tue 2/7/12	Thu 2/9/12	52														
54	Contracting - CW IDIQ	41 days	Fri 2/10/12	Fri 4/6/12															
55	Prepare Solicitation Letter and Package	5 days	Fri 2/10/12	Thu 2/16/12	53														
56	RFP	10 days	Fri 2/17/12	Thu 3/1/12	55														
57	Negotiation	10 days	Fri 3/2/12	Thu 3/15/12	56														
58	Award	5 days	Fri 3/16/12	Thu 3/22/12	57														
59	Bond	10 days	Fri 3/23/12	Thu 4/5/12	58														
60	NTP	1 day	Fri 4/6/12	Fri 4/6/12	59														
61	Construction	276 days	Mon 4/9/12	Mon 4/29/13															
62	Pre-construction Conference	1 day	Mon 4/9/12	Mon 4/9/12	60														
63	Construction	260 days	Tue 4/10/12	Mon 4/8/13	62														
64	Final Inspection	1 day	Tue 4/9/13	Tue 4/9/13	63														
65	Project closeout	14 days	Wed 4/10/13	Mon 4/29/13	64														
66	Project Complete	37 days	Tue 4/30/13	Wed 6/19/13															
67	Physical Closeout	3 days	Tue 4/30/13	Thu 5/2/13	65														
68	Transfer of Remaining Funds	30 days	Fri 5/3/13	Thu 6/13/13	67														
69	Fiscal Closeout	3 days	Fri 6/14/13	Tue 6/18/13	68														
70	Project Closed Out	1 day	Wed 6/19/13	Wed 6/19/13	69														



Project: Perryville Design Schedule
Date: Thu 1/5/12


Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

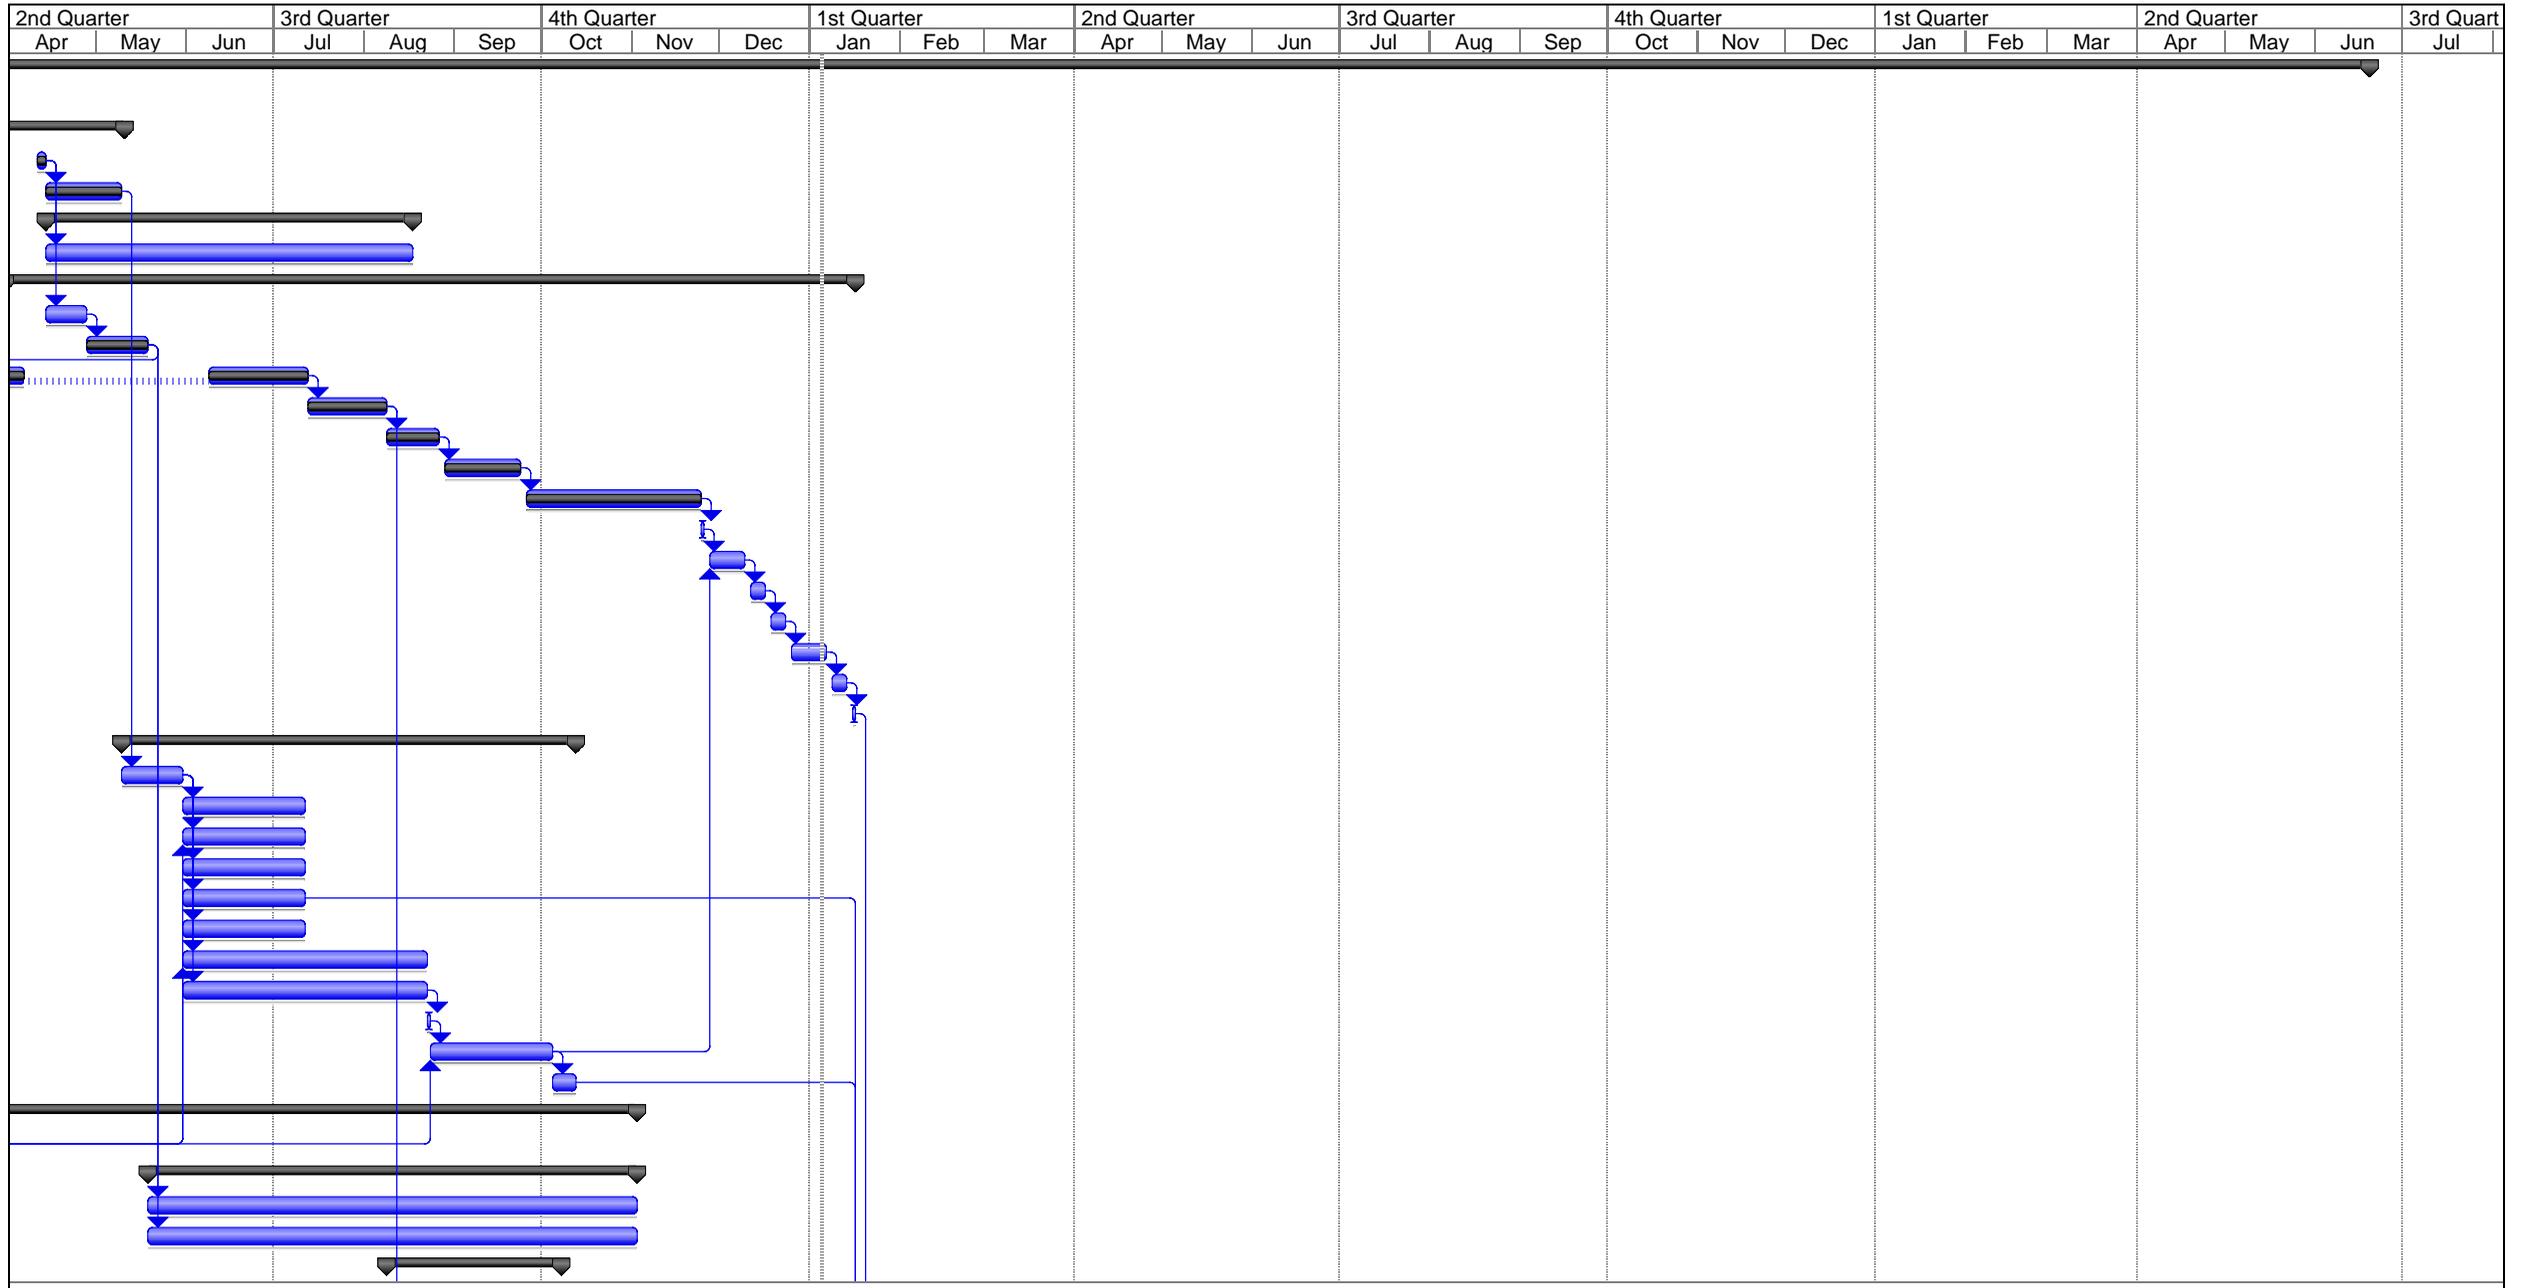

Project: Perryville Design Schedule
Date: Thu 1/5/12

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

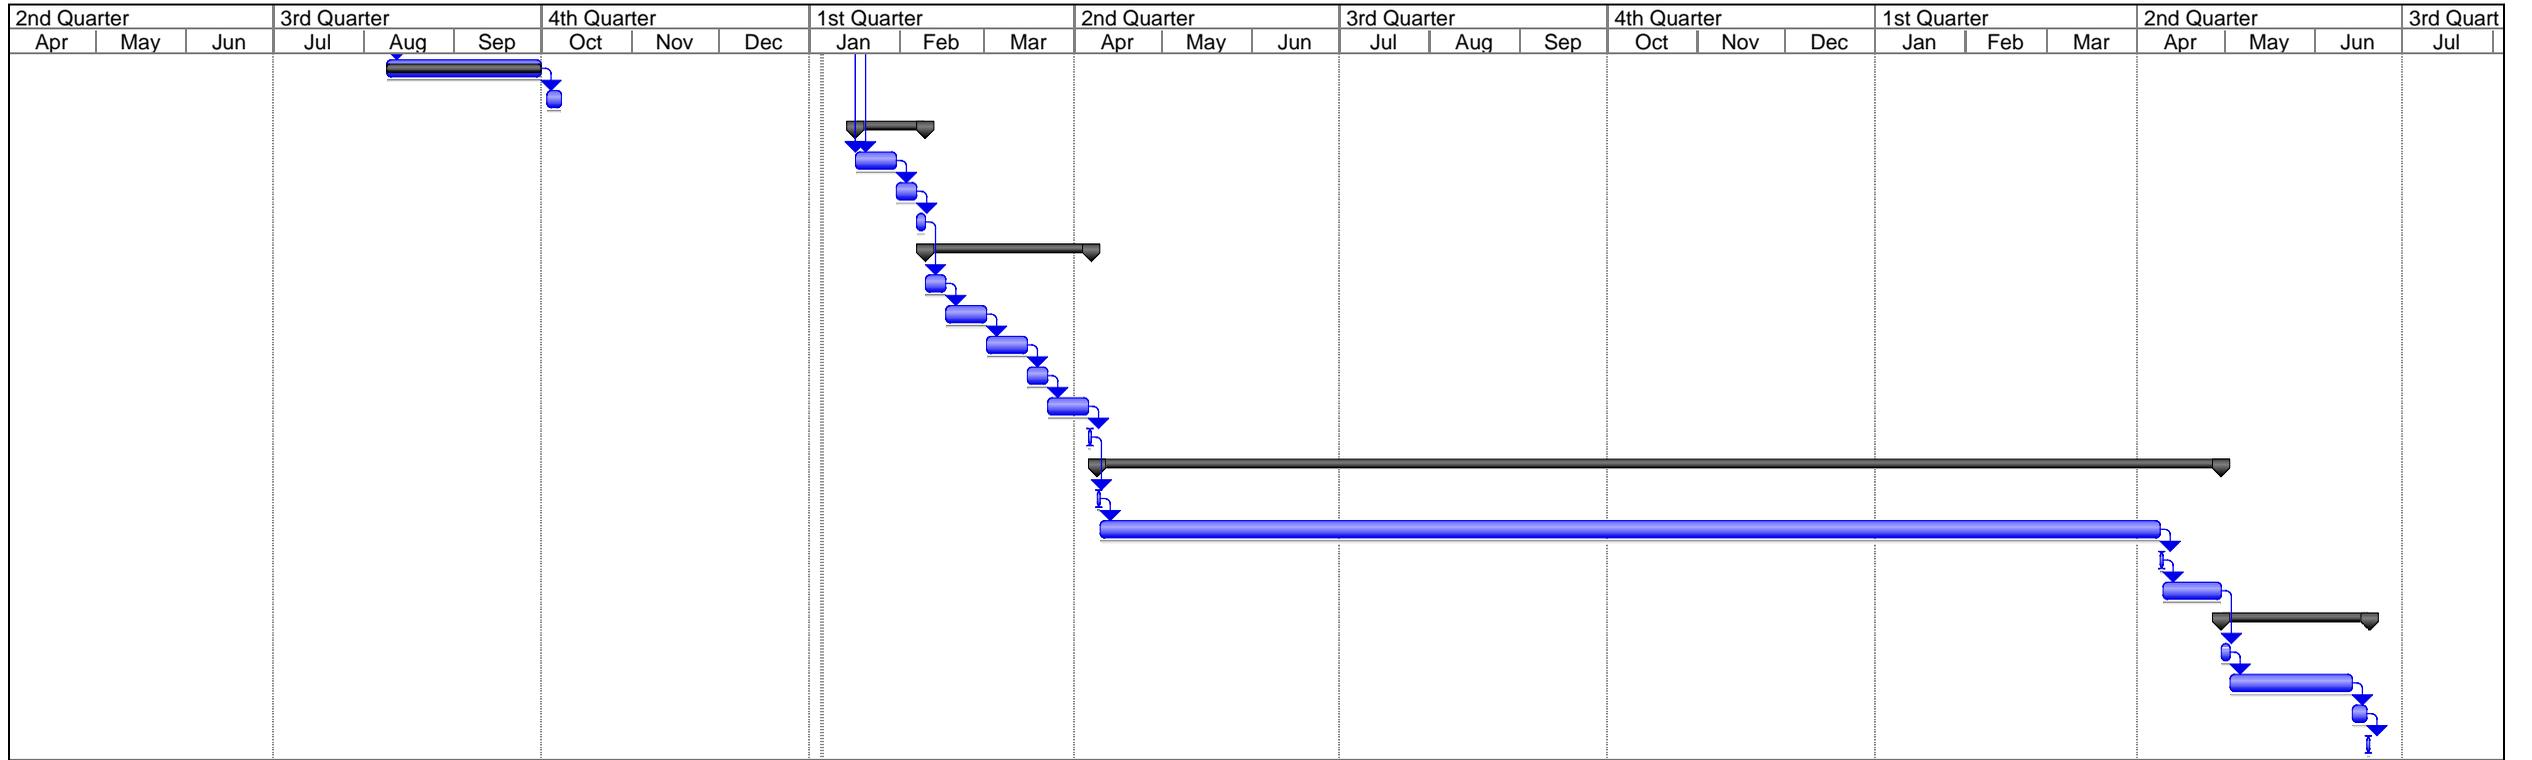

Project: Perryville Design Schedule
 Date: Thu 1/5/12

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
