



**Alaska Native Tribal Health Consortium**

*Department of Environmental Health and Engineering*

**3925 Tudor Centre Drive**

**Anchorage, Alaska 99508**

**Telephone: (907) 729-3600**

**Facsimile: (907) 271-4734**

**STATUS REPORT  
ALASKA RURAL PRIMARY HEALTH CARE FACILITY  
CODE AND CONDITIONS SURVEYS  
AND  
FAST TRACK PROJECT**

**Submitted to:**

**Joel Neimeyer, P.E.**

**Denali Commission**

**Submitted by:**

**ANTHC**

**Project No. 0019-DC-2001-II**

This report updates quarterly progress on the Alaska Rural Primary Health Care Facility planning, design and construction for the quarter ending September 30, 2001.

## **Table of Contents**

### **Section I. Code and Conditions Survey**

Introduction

Summary Groups 1 & 2

List of Groups 3 & 4

Location Maps

YKHC

Larsen Consulting Group

PCD Consulting Group

### **Section II. Fast Track Projects**

Introduction

Progress Reports

Akutan

Alatna

Beaver

Egegik

Kiana

Nanwalek

Nightmute

Nunam Iqua

Pelican

Shageluk

St. George Island

Tazlina

### **Appendix A Summary Sheet**

## **SECTION I**

### **CODE AND CONDITONS SURVEY**

**Code & Conditions Surveys**  
**Alaska Rural Primary Care Facility Planning, Design and Construction**  
**FY 2001 – Project Number 0019-DC-2001-I1**  
**Alaska Native Tribal Health Consortium**

**INTRODUCTION**

After final reports on Code and Conditions Surveys of Group 1 & 2 communities were delivered in July 2001, an effort was initiated to establish an electronic database containing relevant information assembled during the data collection phase and the final report. The following table contains a summary of initial Code and Conditions results.

Following completion of Code and Conditions Surveys of Group 1 & 2 communities, mentioned above, ANTHC made plans to survey additional locations listed in the ARPCFNA as Group 3 & 4 communities. In July 2001 ANTHC requested proposals to perform surveys from four IDIQ Contractors and one previous surveyor of Groups 1 & 2 locations.

Lists of locations to be surveyed were developed which divided Group 3 & 4 communities into five separate geographical regions. Each of the five prospective survey contractors was provided with a different list of communities for one of the regions. Maps of each region accompanied each list. A common scope of services statement also accompanied each RFP. Following distribution of the above a “kick off” informational meeting, a training session to familiarize the IDIQ contractors with survey techniques was held.

On August 22, 2001, while prospective survey teams were preparing their initial proposals, the Denali Commission contacted the Group 3 & 4 communities to secure their cooperation with the proposed survey and their permission for the teams to conduct the surveys. Group 3 & 4 communities included 70 locations. Of these, 56 of the communities contacted responded favorably to the Denali Commission invitation to participate in the survey.

Initial proposals from prospective teams to perform survey work were received at ANTHC September 7, 2001. Subsequent evaluation of proposals and negotiations resulted in the issuance of Notices to Proceed to two of the prospective contractors and to YKHC with surveys of 56 locations. Contractors selected for the work and locations to be surveyed are listed in Appendix A attached. Appendices B, C, and D contain maps of Code and Conditions Survey locations that were awarded.

Draft reports of results from the first locations surveyed are expected in early December 2001.

# SUMMARY Code & Conditions Surveys of Groups & 2 Locations

Clinic Location	Pop.	Exist. Clinic Size SF	Yr. Built	Eligible SF	Recommended Action	Est. Cost	RFP Rec'd @DC
Alakanuk	652	1,861	2000	2,500	Constr Remodel/Addition	\$597,912	Yes
Alatna	35 <sup>1</sup>	154 *	2001	1,500	Compl Constr as Planned	**	N.A.
Ambler	286	1,476	~ 1980	2,000	Constr New Clinic	\$1,030,497	Yes
Arctic Village	138	1,310	1990	2,000	Constr New Clinic	\$878,000	Yes
Birch Creek	35	546	1994	1,500	Constr New Clinic	\$658,500	Yes
Buckland	428	1,152	1989	2,000	Constr New Clinic	\$808,000	Yes
Chalkyitsik	102	768	1994	2,000	Constr New Clinic	\$878,000	Yes
Chignik Lake	136	800	1978	2,000	Constr New Clinic	\$888,000	Yes
Clark's Point	68	786	1963	1,500	Constr New Clinic	\$514,500	Yes
Crooked Creek	137	1,080	2000	2,000	Constr Remodel/Addition	\$609,230	No
Deering	148	820	1978	2,000	Constr New Clinic	\$808,000	Yes
Egegik	117	465	1982	2,000	Constr New Clinic	\$676,000 **	N.A.
Elim	313 <sup>1</sup>	737	~ 1978	2,000	Constr New Clinic	\$938,000 ***	Yes
Evansville/Bettles	24/35	480	1985	1,500	Constr New Clinic	\$648,000	Yes
Game Creek	35 <sup>1</sup>	360	Early 70s	1,500	Constr New Clinic	\$801,000	Yes
Grayling	296 <sup>1</sup>	899	1985	2,000	Constr New Clinic	\$680,000	No
Holy Cross	227	1,080	1999	2,000	Constr Renov/Addn	\$456,160	Yes
Hooper Bay	1,028	2,132	1989	2,500	Constr New Clinic	\$1,352,932	No
Hughes	80	768	1993	1,500	Constr New Clinic	\$579,000	Yes
Huslia	293 <sup>1</sup>	858	~ 1960	2,000	Constr New Clinic	\$866,000	Yes
Lower Kalskag	310	1,400	2000	2,000	Constr Renov/Addn	\$399,657	N.A.
Kaltag	230 <sup>1</sup>	1,125	1994	2,000	Constr New Clinic	\$772,000	Yes
Kasigluk	543	1,372	1984	2,500	Constr New Clinic	\$1,127,500	No
Kiana	398	1,560	1984	2,000	Constr New Clinic	\$776,000 **	N.A.
Kivalina	366	1,064	1981	2,000	Constr New Clinic	\$808,000	Yes
Kobuk	94 <sup>2</sup>	1,304	1978	2,000	Constr New Clinic	\$808,000	Yes
Lk Minchumina	38	2,256	~ 1970	1,500	Constr New Clinic	\$523,500	No
Minto	248	1,045	1983	2,000	Constr New Clinic	\$864,000	Yes
Newtok	284	566	1989	2,000	Constr New Clinic	\$902,000	Yes
Nikolai	105	525	1983	2,000	Constr New Clinic	\$746,000	Yes
Noatak	423	1,242	1978	2,000	Constr New Clinic	\$966,000	Yes
Nondalton	224	1,216	1992	2,000	Constr New Clinic	\$880,060	No
Nulato	336	959	1978	2,000	Constr New Clinic	\$772,000	Yes
Perryville	102	800	1990	2,000	Constr New Clinic	\$878,000	Yes
Pilot Station	544	1,200	1990	2,500	Constr New Clinic	\$850,000	Yes
Port Alexander	86	54	1990	1,500	Constr New Clinic	\$648,000	Yes
Port Alsworth	88	1,450	~ 2000	1,500	Complt Prtn unf mtl bldg	\$353,181	Yes
Russian Mission	311	1,280	1987	2,000	Constr New Clinic	\$684,000	Yes
Scammon Bay	484	1,058	1987	2,000	Constr New Clinic	\$902,000	Yes
Shungnak	255	1,284	1978	2,000	Constr New Clinic	\$808,000	Yes
Stebbins	547 <sup>1</sup>	1,640	Unknown	2,500	Constr New Clinic	\$847,500	Yes
Steven Village	92	680	~ 1992	1,500	Constr New Clinic	\$657,000	Yes
Takotna	48	640	~ 1990	1,500	Constr New Clinic	\$668,000	Yes
Venetie =	232	1,250	1988	2,000	Constr New Clinic	\$866,000	N.A.

\*New 915 SF clinic under construction

\*\*Currently funded "Fast-Track" Project

\*\*\*Currently under construction

<sup>1</sup> Current Population

<sup>2</sup> Current Population Exceeds 100

= GR 3 Community

## LIST OF GROUP 3 & 4 CODE AND CONDITONS SURVEY LOCATIONS AWARDED

YKHC

Larsen Consulting Group


PDC  
Consulting  
Engineer

Akiak  
Atmaultuak  
Chefornak  
Chignik  
Chitna  
Chuathbaluk  
Dot Lake  
Eek  
Goodnews Bay  
Gulkana  
Illiamna  
Kipnuk  
Kokhanok  
Kwigilingok  
Levelok  
Lime Village  
Marshall  
Mekoryuk  
Mountain Village  
Napaskiak  
Newhalen  
Oscarville  
Platinum  
Sleetmute  
Stony River  
Tetlin  
Tuntutuliak  
Tununak  
Wasilla

Akhiok  
Anchor Point  
Chenega Bay  
Cooper Landing  
Ekwok  
False Pass  
Hope  
Koliginek  
Larsen Bay  
Manakotak  
Nikolaevsk  
Port Graham  
Twin Hills  
Tyonek

Allakaket  
Circle  
Gambell  
Golovin  
Koyuk  
Koyukuk  
McGrath  
Nenana  
Ruby  
Shishmaref  
Teller  
White Mountain

# LarsenConsultingGroup

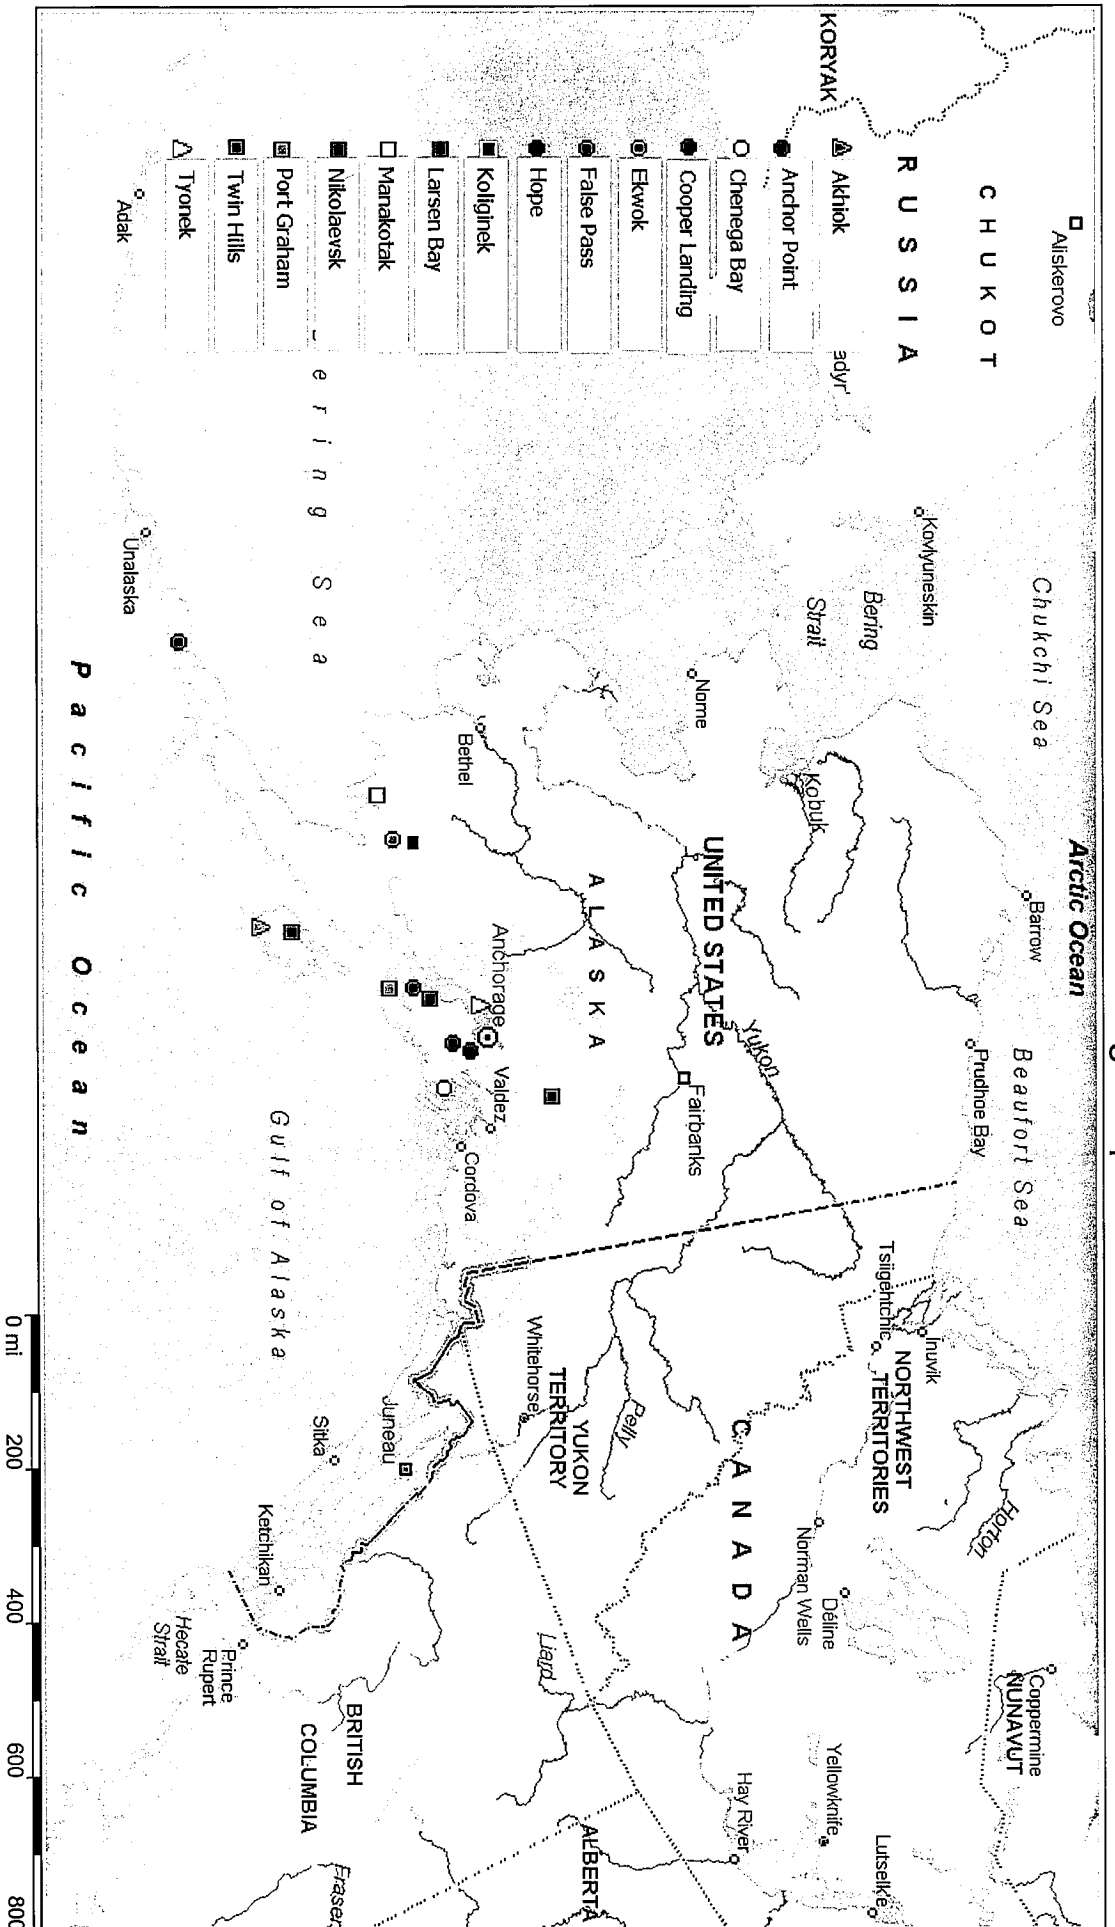

**R U S S I A**  
**C H U K O T**

**U N I T E D S T A T E S**  
**A L A S K A**  
**Y U K O N T E R R I T O R Y**  
**C A N A D A**  
**N O R T H W E S T T E R R I T O R I E S**  
**B R I T I S H C O L U M B I A**

**B e r i n g S e a**  
**G u l f o f A l a s k a**  
**P a c i f i c O c e a n**

**Chukchi Sea**  
**Beaufort Sea**

**Barrow**  
**Nome**  
**Fairbanks**  
**Anchorage**  
**Valdez**  
**Cordova**  
**Juneau**  
**Sitka**  
**Ketchikan**  
**Prince Rupert**


**White Mountain**  
**Teller**  
**Shishmaref**  
**Ruby**  
**Nenana**  
**McGrath**  
**Koyukuk**  
**Koyuk**  
**Golovin**  
**Gambell**  
**Circle**  
**Allakaket**

**Bering Strait**  
**Kopuk**  
**Yukon**  
**Pelly**  
**Whitehorse**  
**Lia**

**Unalakleet**  
**Adak**

**0 mi**  
**200**  
**400**  
**600**  
**800**



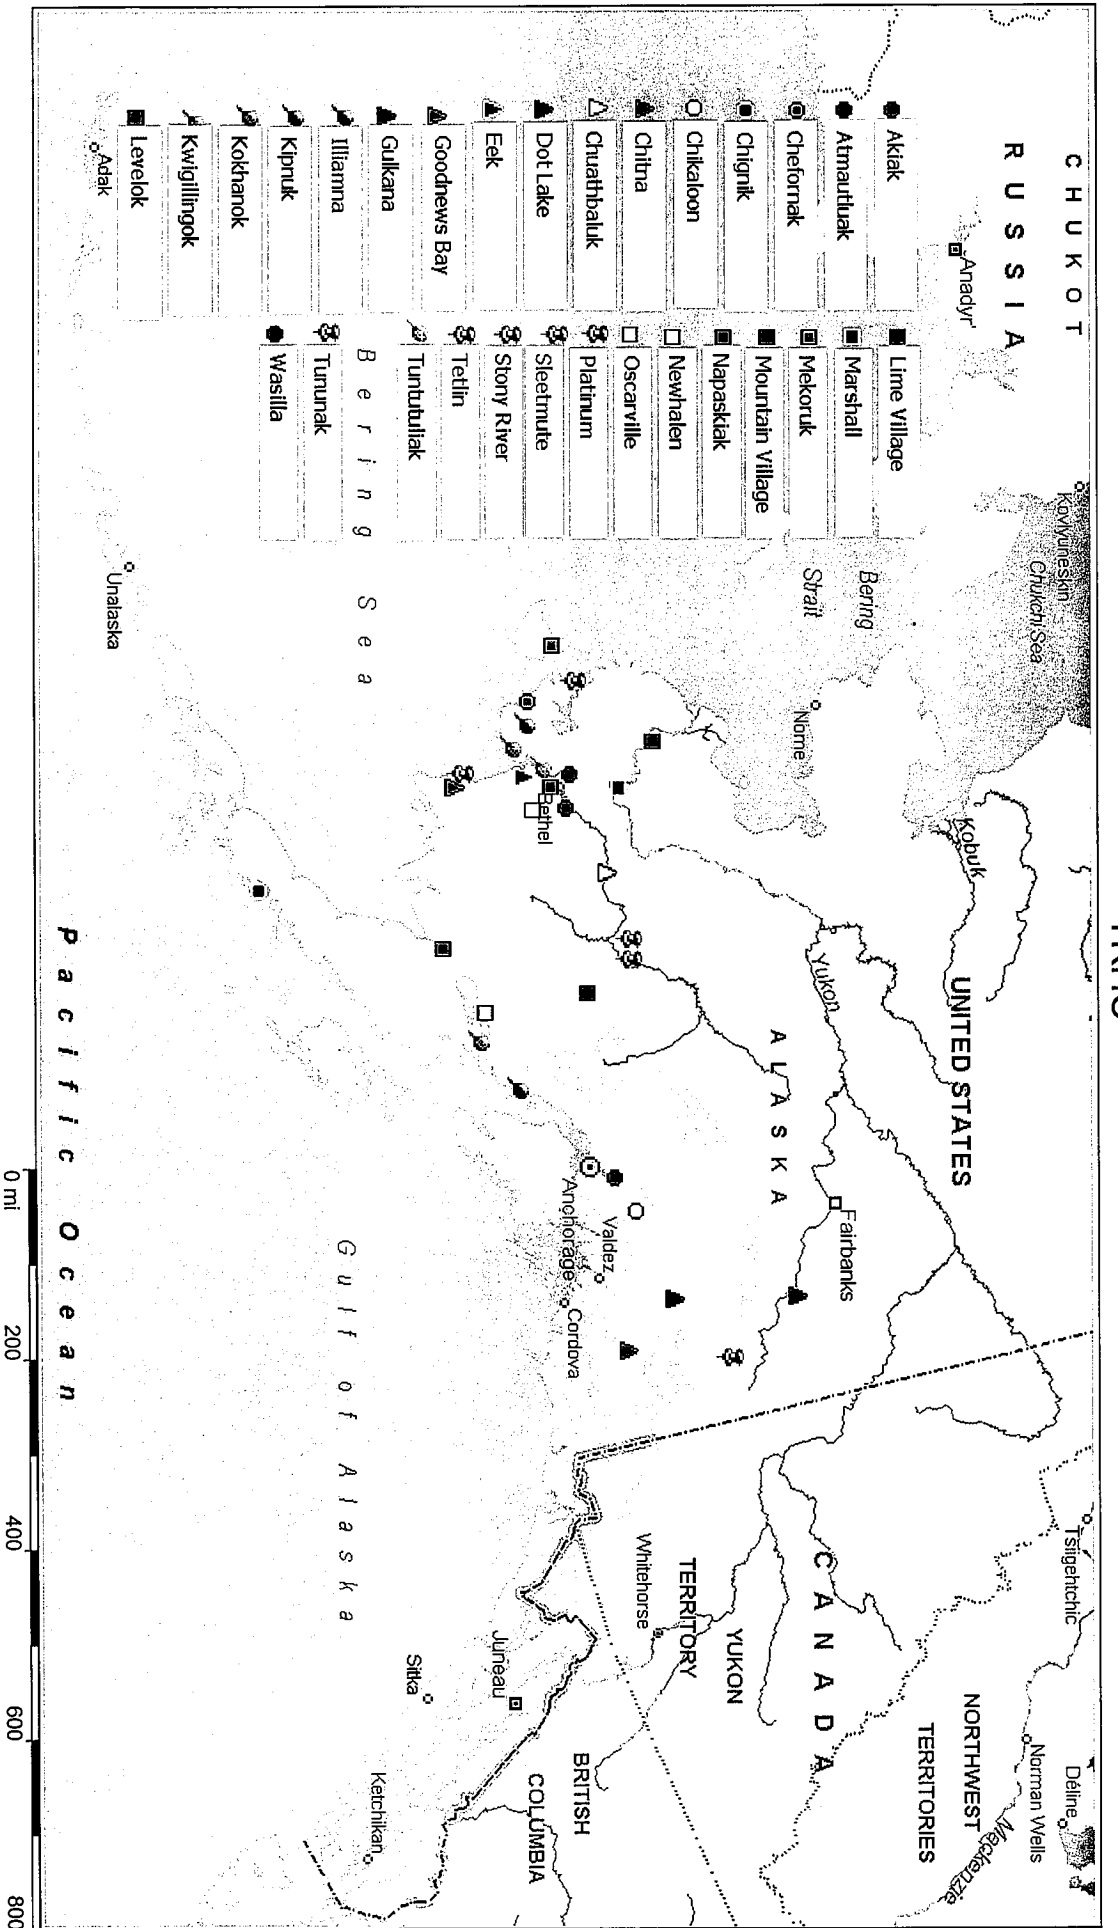

**SECTION II**  
**FAST TRACK PROJECTS**

## INTRODUCTION

A Memorandum of Understanding (MOU) issued by the Denali Commission in March 2001 preceded the current Financial Assistance Award and defines, in detail, the Alaska Native Tribal Health Consortium (ANTHC) roles and responsibilities in managing the development of Alaska Rural Primary Health Care Facilities. Those duties defined in part C pages 4 and 5 of the MOU have been actively developed and worked on by the ANTHC and our consultants during the quarter ending June 30, 2001.

Since the March 20, 2001 issuance of the subject Financial Assistance Award the ANTHC has developed and implemented a system for surveying Primary Health Care Facilities in 120 rural Alaskan communities. The list of communities was initially divided according to priorities of perceived need and numbered sequentially. Communities in Groups 1 and 2 were contacted with Letters of Agreement identifying the ANTHC as the commission's agent allowing for code and condition surveys of existing clinics and/or tribal participation in project planning efforts.

Using survey methods jointly developed by the ANTHC and the Regional Health Care organizations 41 clinics in participating communities were surveyed.

The Denali Commission subsequently requested proposals from owners and operators of clinics in participating communities. The resulting proposals were evaluated and value assigned indicative of the relative perceived need for renovation or replacement of existing clinics.

As a result of recommendations made by the proposal report evaluators, the Denali Commission awarded twelve (12) Financial Assistance Grant for "Fast Track Projects." This report details the ANTHC activity in support of these 12 projects.\*

\*See Appendix A for a summary of activities to date.

**Location: Akutan**

ANTHC Code: AN 01-G02

Sub Recipient: City of Akutan

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: Eastern Aleutian Tribes

Denali Commission Funding: \$271,024

Total Project Cost: \$595,179

**Scope:** Replacement clinic construction project planned to be procured through Force Account Method. Archaeological survey may be required. Application for review by State of Alaska Fire Marshall filed 4/5/01. Small clinic design by Tom Huntington of Alaska Building Consultants, 2314 Douglas Hwy, Douglas, Alaska, 99824 (email: IbuildinAK@aol.com). Construction to start June 01, 2001.

**Project History:** On May 14, 2001 the Denali Commission Steering Committee forwarded Akutan's applications for funding to the commission. Akutan's application was rated the highest score of those submitted.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

**Accomplishments:** On July 23, 2001 we received a signed copy of the Financial Assistance Sub-Award Agreement from the City of Akutan acknowledging terms of the award for the project.

An Environmental Analysis of the project is nearing completion.

**Location: Alatna**

ANTHC Code: AN 01-G01

Sub Recipient: Alatna Tribal Council

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: TCC

Denali Commission Funding: \$291,000\*

Total Project Cost: \$1,696,000

**Scope:** The planned clinic will occupy space in a new multi-purpose building. The clinic will occupy 925 sq. ft. of 2,548 sq. ft. total. The new building also contains the water treatment plant and the village washeteria. Total funds from other sources \$1,405,000.

**Project History:** On May 14, 2001 the Denali Commission Steering Committee forwarded Alatna's applications for funding to the commission. Alatna's application was rated with 84 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

\*Funding granted includes ANTHC's construction management fee of \$62,854.

**Accomplishments:** The funding for clinic construction has been incorporated into an existing funding agreement for construction of the new multipurpose building.

We have completed the insulated refrigerated gravel pad for the building and additional work will start in the spring.

**Location: Beaver**

ANTHC Code: AN 01-G07

Sub Recipient: Beaver Tribal Council

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: TCC

Denali Commission Funding: \$154,900

Total Project Cost: \$915,029

Scope: Funds granted are to complete work on project under construction by October 1, 2001. Project was estimated to be 80% complete on May 25, 2001. Funds expended thru 5/25/2001.....\$760,129.

Total clinic space: 5,100 sq. ft. Cost per sq. ft. = \$149.49

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Beaver's applications for funding to the commission. Beaver's application was rated with 75 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

Accomplishments: On August 8 we received and processed an initial request for funding in the amount of \$50,045.00.

The Environmental Analysis of the project is nearing completion.

**Location: Egegik**

ANTHC Code: AN-01G04

Sub Recipient: Egegik Village Council

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: Bristol Bay Area Health Corp.

Denali Commission Funding: \$241,000

Total Project Cost: \$503,984

**Scope:** New Egegik Clinic Facility – new construction of a 58' x 42' (2,436 sq. ft.) structure on City owned land adjoining the old airport. State of Alaska, Lake and Peninsula Borough, and the City of Egegik have guaranteed the balance of funds required to complete project. Karluk Design served as Architects and Engineers for the project. The Fire Marshall's permit for the project was issued 12/28/98 has expired and must be renewed. An environmental assessment is in progress.

**Project History:** On May 14, 2001 the Denali Commission Steering Committee forwarded Egegik's applications for funding to the commission. Egegik's application was rated with 80 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

**Accomplishments:** On July 23, 2001 we received the signed Financial Assistance Award Agreement from the Egegik Tribal Council acknowledging the terms of the award for the project.

The Environmental Analysis of the project is nearing completion.

**Location: Kiana**

ANTHC Code: AN 01-G08

Sub Recipient: Maniilaq Association

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: Maniilaq Assoc.

Denali Commission Funding: \$700,000

Total Project Cost: \$947,134

Scope: New building to be built in Maniilaq owned land.

C B Bettisworth & Co of Fairbanks are Architects for the Project. The HMS, Inc., prepared the construction estimate based on force account process. The Fire Marshall permit was issued on 7/24/00.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Kiana's applications for funding to the commission. Kiana's application was rated with 68 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On July 23, 2001 we received the signed Financial Assistance Award Agreement from the Egegik Tribal Council acknowledging the terms of the award for the project.

The Environment Analysis of the project is nearing completion.



**Location: Nanwalek**

ANTHC Code: AN 01-G09

Sub Recipient: Nanwalek IRA Council

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: Chugachmuit

Denali Commission Funding: \$244,812

Total Project Cost: \$344,812

Scope: Nanwalek Health Clinic Renovation. Renovate space (formerly occupied by Head Start) adjacent to existing clinic. Total area to increase to 2,088 sq. ft. The Nanwalek IRA Council donated land and the existing building valued at \$100,000 as their contribution to the project.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Nanwalek's applications for funding to the commission. Nanwalek's application was rated with 67 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On July 19, 2001 we received the signed Financial Assistance Sub-Award agreement acknowledging the terms of the award for the project.

On August 17, 2001 we received and processed the initial request for funding in the amount of \$75,832. The Environmental Analysis of the project is nearing completion.

**Location: Nightmute**

ANTHC Code: AN 01-G03

Sub Recipient: YKHC

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: YKHC

Denali Commission Funding: \$310,942

Total Project Cost: \$

Scope: New clinic (1,944 sq. ft.) construction project planned to replace existing clinic. The project is to be procured through Force Account Method. Plans for the project are by Winchester Alaska, Inc.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Nightmute's applications for funding to the commission. Nightmute's application was rated with 83 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On August 30, 2001 we received the signed Financial Assistance Sub-Award Agreement acknowledging terms of the award for the project.

The Environmental Analysis of the project is nearing completion.

**Location: Nunam Iqua**

ANTHC Code: AN 01-G10

Sub Recipient: YKHC

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: YKHC

Denali Commission Funding: \$786,344

Total Project Cost: \$981,229

Scope: New construction on city lot (67' x 28'+ arctic entry 7' x 9'9" = 1,944 sq. ft.). Plans by Winchester Alaska, Inc. State of Alaska Fire Marshall's permit issued 04/22/01.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Nunam Iqua's application for funding to the commission. Nunam Iqua's application was rated with 64 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On August 30, 2001 we received the signed Financial Assistance Sub-Award Agreement acknowledging terms of the award for the project.

The Environmental Analysis of the project is nearing completion.

**Location: Pelican**

ANTHC Code: AN 01-G11

Sub Recipient: City of Pelican

Period Ending: 9/30/2001

Pass-through Entity: ANTHC

Region: SEARHC

Denali Commission Funding: \$10,588

Total Project Cost: \$13,235

Scope: Purchase and installation of a new furnace and refurnish space to provide additional exam room. Twenty percent matching funds are to be provided by the City of Pelican.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Pelican's application for funding to the commission. Pelican's application was rated with 64 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On July 30, 2001 we received a signed copy of the Financial Assistance Sub-Award Agreement acknowledging terms of the award for the project.

On August 27, 2001 we received and processed a request for funding in the amount of \$10,344.

**Location: Shageluk**

ANTHC Code: AN 01-G12

Sub Recipient: YKHC

Period Ending: 6/30/2001

Pass-through Entity: ANTHC

Region: YKHC

Denali Commission Funding: \$655,327

Total Project Cost: \$976,370

Scope: New building, 28 feet by 67 feet, scheduled to start construction 9/30/01. To be constructed on a platted city lot leased to the Shageluk IRA council for 30 years and served by an existing utility system. The existing clinic is to be abandoned. Plans for the new building were completed by Winchester Alaska, Inc. YKHC to use force account method.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Shageluk's applications for funding to the commission. Shageluk's application was rated with 63 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On August 30, 2001 we received a signed copy of the Financial Assistance Sub-Award agreement acknowledging terms of the award for the project.

The Environmental Analysis of the project is nearing completion.

**Location: St. George Island**

ANTHC Code: AN 01-G05

Sub Recipient: Pribilof Island Aleut Community

Period Ending: 6/30/2001

Pass-through Entity: ANTHC

Region: Aleutian/Pribilof Islands Assoc., Inc.

Denali Commission Funding: \$ 67,956

Total Project Cost: \$538,774

Scope: Renovation and repair of existing building. Entire amount provided by the Denali Commission funding is scheduled to purchase non-expendable equipment for the repaired clinic. Ahtna Enterprises, are construction management consultants and contractor for the project. Polar Consultants prepared the construction drawings. DOWL Engineering prepared the cost estimate.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded St. George Island's application for funding to the commission. St. George Island's application was rated with 79 points of a possible 100 by the steering committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On August 7, 2001 we received a signed copy of the Financial Assistance Sub-Award Agreement acknowledging terms of the award for the project.

The Environmental Analysis of the project is nearing completion.

**Location: Tazlina**

ANTHC Code: AN 01-G10

Sub Recipient: Native Village of Tazlina

Period Ending: 6/30/2001

Pass-through Entity: ANTHC

Region: Copper River Native Assoc.

Denali Commission Funding: \$100,000

Total Project Cost: \$253,000

Scope: Move existing donated building from present location to new location (approximately ½ mile) and renovate to provide new clinic. Project needs professional plans for the work and the Fire Marshall's review and approval.

Project History: On May 14, 2001 the Denali Commission Steering Committee forwarded Tazlina's application for funding to the commission. Tazlina's application was rated with 77 points of a possible 100 by the Steering Committee.

On June 21, 2001 the ANTHC was notified that the Denali Commission had approved the requested funding.

An Environmental Analysis is in progress.

Accomplishments: On July 24, 2001 we received a signed copy of the Financial Assistance Sub-Award Agreement acknowledging terms of the award for the project.

On September 19, 2001 we processed the initial request for funding from the Native village of Tazlina for the amount of \$30,000. The request for funding contained a summary schedule projecting target completion date for the project April 30, 2002.

Environmental Analysis of the project is nearing completion.

**Summary Sheet**  
**Group 3 & 4**  
**Code and Conditions Survey**

Project Number	Description	Sub Recipient	DC Approved Funding Sub Award Amt.	Sub-Award Acknowledgement Received	Start of On-Site Construction	Scheduled B.O.D.	Initial Draw Requested	Remarks
AN 01-G01	Alatna Clinic As Part Of Multi-purpose Facility	Altna Tribal Council	\$291,000.00		7/1/01	12/1/02		
AN 01-G02	Akutana Clinic Replacement	City of Akutana	\$271,024.00	7/23/01	6/15/01	6/15/02		
AN 01-G03	Nightnute Primary Health Care Facility Replacement	YKHC	\$310,942.00	8/30/01	On or Before 9/24/01			
AN 01-G04	Egegik Clinic Replacement	Egegik Village Council	\$241,000.00	7/23/01	On or Before 9/10/01			
AN 01-G05	St. George Traditional Council Clinic-Equipment	Pribilof Island Aleut Community	\$67,956.00	8/7/01	Equipment on order *			
AN 01-G06	Tazlina Health Clinic Renovation to Provide First Timer Service	Native Village of Tazlina	\$100,000.00	7/24/01	Ongoing 8/1/01		\$30,000Rd	
AN 01-G07	Beaver Community Health Clinic-Clinic in Multi-Purpose Facility	Beaver Tribal Council	\$154,900.00	7/1 1/01	Ongoing 8/1/01	Est. B.O.D. 1/1/02	\$50,045 Rd \$37,116.00	
AN 01-G08	Kiana Clinic Replacement	Manilaq Association	\$700,000.00	8/28/01	Ongoing 8/1/01			
AN 01-G09	Nanwalek Clinic Renovation	Nanwalek IRA Council	\$244,812.00	7/19/01	Start 9/15/01	Est. B.O.D. 5/30/02	\$75,832 Rd 8/17/01	
AN 01-G10	Nunam Iqua Clinic New Project	YKHC	\$786,344.00	8/30/01	On or Before 9/24/01			
AN 01-G11	Pelican Clinic Renovation	City of Pelican	\$10,588.00	6/30/01	On or Before 9/1/01	On or Before 11/15/01	\$10,344.48 Rd 8/28/01	
AN 01-G12	Shageluk Primary Health Care Facility-New Clinic	YKHC	\$655,327.00	8/30/01	On or Before 9/24/01			



Quarterly Report of Activities On "Fast Track" Projects  
 Alaska Rural Primary Care Facility Planning, Design and Construction - FY 01  
 Project Number 0019-DC-2001-11  
 Alaska Native Tribal Health Consortium

Project Number	Description	Sub Recipient	Denali Commission Approved Funding Sub Award Amount	Sub-Award Acknowledgment Received	Start of On-Site Construction	Scheduled B.O.D.	Draws Requested	Remarks
AN 01-G01	Alatna Clinic As Part Of Multi-purpose Facility	Alatna Tribal Council	\$228,146	pending	7/1/2001	12/1/2002		ANTHC lead, foundation complete
AN 01-G02	Akutan Clinic/Replacement	City of Akutan	\$271,024	7/23/2001	6/15/2001	6/15/2002		
AN 01-G03	Nightmute Primary Health Care Facility Replacement	YKHC	\$310,742	8/30/2001	On-going	4/1/2002	\$108,759.20	Draw being processed, 35% complete
AN 01-G04	Egegik Clinic Replacement	Egegik Village Council	\$241,000	7/23/2001	Early 2002	On or before 9/10/02		Pre-bid conference on Dec. 14, 2001
AN 01-G05	St George Traditional Council Clinic-Equipment	Pribilof Island Aleut Community	\$56,158	8/7/2001	Equipment on order *			
AN 01-G06	Tazlina Health Clinic Renovation to Provide First Time Service	Native Village of Tazlina	\$100,000	7/24/2001	ONGOING 8/01/01		\$30,000.00	
AN 01-G07	Beaver Community Health Clinic- Clinic in Multi-purpose Facility	Beaver Tribal Council	\$154,900	7/11/2001	ONGOING 8/01/01	EST. B.O.D. 1/1/02	\$98,161.00	
AN 01-G08	Kiana Clinic Replacement	Maniilaq Association	\$700,000	8/28/2001	ONGOING 8/01/01			75% complete
AN 01-G09	Nanwalek Clinic Renovation	Nanwalek IRA Council	\$244,812	7/19/2001	9/15/01	EST. B.O.D. 5/30/02	\$75,832.00	
AN 01-G10	Nunam Iqua Clinic New Project	YKHC	\$786,344	8/30/2001	On-going	4/1/2002	\$275,550.40	Draw being processed, 35% complete
AN 01-G11	Pelican Clinic Renovation	City of Pelican	\$10,588	6/30/2001	9/1/01	Est. 11/15/01	\$10,344.48	
AN 01-G12	Shageluk Primary Health Care Facility-New Clinic	YKHC	\$655,327	8/30/2001	On-going	4/1/2002	\$232,864.45	Draw being processed, 35% complete
	Totals		\$3,759,041				\$831,512	
							Updated 12/12/01	

Quarterly Report of Activities On "Fast Track" Projects  
 Alaska Rural Primary Care Facility Planning, Design and Construction - FY 01  
 Project Number 0019-DC-2001-11  
 Alaska Native Tribal Health Consortium

Project Number	Description	Sub Recipient	Denali Commission Approved Funding Sub Award Amount	Sub-Award Acknowledgment Received	Start of On-Site Construction	Scheduled B.O.D.	Draws Requested	Remarks
AN 01-G01	Alatna Clinic As Part Of Multi-purpose Facility	Alatna Tribal Council	\$228,146	pending	7/1/2001	12/1/2002		ANTHC lead, foundation complete
AN 01-G02	Akutan Clinic Replacement	City of Akutan	\$271,024	7/23/2001	6/15/2001	6/15/2002		
AN 01-G03	Nightmute Primary Health Care Facility Replacement	YKHC	\$310,742	8/30/2001	On-going	4/1/2002	\$108,759.20	Draw being processed, 35% complete
AN 01-G04	Egegik Clinic Replacement	Egegik Village Council	\$241,000	7/23/2001	Early 2002	On or before 9/10/02		Pre-bid conference on Dec. 14, 2001
AN 01-G05	St George Traditional Council Clinic-Equipment	Pribilof Island Aleut Community	\$56,158	8/7/2001	Equipment on order *			
AN 01-G06	Tazlina Health Clinic Renovation to Provide First Time Service	Native Village of Tazlina	\$100,000	7/24/2001	ONGOING 8/01/01		\$30,000.00	
AN 01-G07	Beaver Community Health Clinic- Clinic in Multi-purpose Facility	Beaver Tribal Council	\$154,900	7/11/2001	ONGOING 8/01/01	EST. B.O.D. 1/1/02	\$98,161.00	
AN 01-G08	Kiana Clinic Replacement	Maniilaq Association	\$700,000	8/28/2001	ONGOING 8/01/01			75% complete
AN 01-G09	Nanwalek Clinic Renovation	Nanwalek IRA Council	\$244,812	7/19/2001	9/15/01	EST. B.O.D. 5/30/02	\$75,832.00	
AN 01-G10	Nunam Iqua Clinic New Project	YKHC	\$786,344	8/30/2001	On-going	4/1/2002	\$275,550.40	Draw being processed, 35% complete
AN 01-G11	Pelican Clinic Renovation	City of Pelican	\$10,588	6/30/2001	9/1/01	Est. 11/15/01	\$10,344.48	
AN 01-G12	Shageluk Primary Health Care Facility-New Clinic	YKHC	\$655,327	8/30/2001	On-going	4/1/2002	\$232,864.45	Draw being processed, 35% complete
	Totals		\$3,759,041				\$831,512	
							Updated 12/12/01	

Quarterly Report of Activities On "Fast Track" Projects  
 Alaska Rural Primary Care Facility Planning, Design and Construction - FY 01  
 Project Number 0019-DC-2001-11  
 Alaska Native Tribal Health Consortium

Project Number	Description	Sub Recipient	Denali Commission Approved Funding Sub Award Amount	Sub-Award Acknowledgment Received	Start of On-Site Construction	Scheduled B.O.D.	Draws Requested	Remarks
AN 01-G01	Alatna Clinic As Part Of Multi-purpose Facility	Alatna Tribal Council	\$228,146	pending	7/1/2001	12/1/2002		ANTHC lead, foundation complete
AN 01-G02	Akutan Clinic Replacement	City of Akutan	\$271,024	7/23/2001	6/15/2001	6/15/2002		
AN 01-G03	Nightmute Primary Health Care Facility Replacement	YKHC	\$310,742	8/30/2001	On-going	4/1/2002	\$108,759.20	Draw being processed, 35% complete
AN 01-G04	Egegik Clinic Replacement	Egegik Village Council	\$241,000	7/23/2001	Early 2002	On or before 9/10/02		Pre-bid conference on Dec. 14, 2001
AN 01-G05	St George Traditional Council Clinic-Equipment	Pribilof Island Aleut Community	\$56,158	8/7/2001	Equipment on order *			
AN 01-G06	Tazlina Health Clinic Renovation to Provide First Time Service	Native Village of Tazlina	\$100,000	7/24/2001	ONGOING 8/01/01		\$30,000.00	
AN 01-G07	Beaver Community Health Clinic- Clinic in Multi-purpose Facility	Beaver Tribal Council	\$154,900	7/11/2001	ONGOING 8/01/01	EST. B.O.D. 1/1/02	\$98,161.00	
AN 01-G08	Kiana Clinic Replacement	Manilaq Association	\$700,000	8/28/2001	ONGOING 8/01/01			75% complete
AN 01-G09	Nanwalek Clinic Renovation	Nanwalek IRA Council	\$244,812	7/19/2001	9/15/01	EST. B.O.D. 5/30/02	\$75,832.00	
AN 01-G10	Nunam Iqua Clinic New Project	YKHC	\$786,344	8/30/2001	On-going	4/1/2002	\$275,550.40	Draw being processed, 35% complete
AN 01-G11	Pelican Clinic Renovation	City of Pelican	\$10,588	6/30/2001	9/1/01	Est. 11/15/01	\$10,344.48	
AN 01-G12	Shageluk Primary Health Care Facility-New Clinic	YKHC	\$655,327	8/30/2001	On-going	4/1/2002	\$232,864.45	Draw being processed, 35% complete
	Totals		\$3,759,041				\$831,512	
							Updated 12/12/01	

\* EQUIPMENT GRANT

12/13/2001

Fast Track Project Status 12Dec01.xls
