



Boiler 1 burner blew off of unit prior to our arrival.



New burner installed on boiler.




Both boilers up and running after adjusting flame, and water and high limit to work with waste heat system.



Plate heat exchanger for waste heat system from generator plant.



Youngs in line heat exchanger, wrong unit for this application, changed this one out with plate heat exchanger.

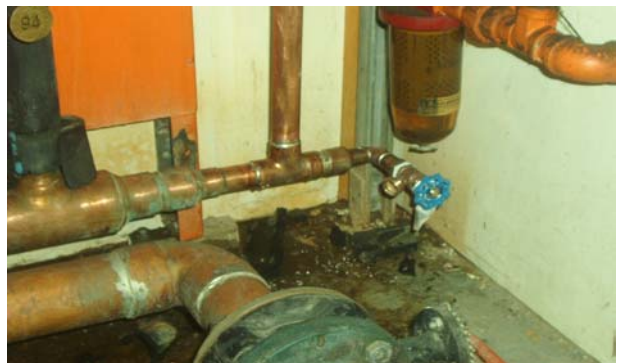

Added boiler drain to bottom of return manifold in boiler room, to allow bleeding of system.
