PRO-WEST Contractors, LLC
Professional Construction Services For Rural Alaska
P.O. Box 870129 prowestcontractors@gmail.com
Wasilla, Alaska 99687 Phone/Fax: (907) 373-8055

Maniilaq Association

P.O. Box 256 Kotzebue, **Alaska 99**752

Project Managed by WHPacific, Inc

SUBMITTAL SUMMARY SHEET

PROJECT: Noorvik Cemetery Road, BIA Route 1047 PROJECT NO.: WHP 524401

1 ITEM NO.: 108

2 SPECIFICATION PARAGRAPH: 1.03(1)

3 DRAWING NO.:

4 NAME OF ARTICLE:

Progress Schedule

5 MANUFACTURER:

6 SIZE, CAPACITY, OR RATING:

7 CATALOG NO.:

8 SPARE PARTS AVAILABLE FROM:

9 GUARANTEE PROVIDED BY:

CONTRACTOR: NAME: Pro-West Contractors LLC

ADDRESS: P. O. Box 870129

Wasilla, AK 99687

PHONE: (907) 373-8055 FAX: (907) 373-8065

SUBCONTRACTOR NAME: NA

ADDRESS:

PHONE: FAX

DATE: 6-3-2011

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	642(1) Construction Survey	7 days	Wed 7/20/11	Wed 7/27/11		
2	640(1) Mobilization	1 day	Mon 8/1/11	Mon 8/1/11		
3	633(1) Silt Fence	53 days	Tue 8/2/11	Sat 10/1/11	2SS+1 day	
4	643(1) Traffic Maintenance Signs	1 day	Tue 8/2/11	Tue 8/2/11	2	
5	201(1A) Clearing	10 days	Wed 8/3/11	Sat 8/13/11	1	
6	203(5A) Manufacture Borrow, Type A	14 days	Wed 8/3/11	Thu 8/18/11		
7	202(4) Removal of Culvert Pipe	2 days	Wed 8/3/11	Thu 8/4/11		
8	603 Install Culverts	21 days	Thu 8/4/11	Sat 8/27/11	7SS+1 day	
9	203(5A) Hauling/Placing Borrow, Type A	21 days	Thu 8/4/11	Sat 8/27/11	8SF	
10	203(5C) Manufacture Borrow, Type C	20 days	Wed 8/3/11	Thu 8/25/11		
11	203(5C) Hauling/Placing Borrow, Type C	24 days	Thu 8/4/11	Wed 8/31/11	10SS+1 day	
12	635(1) Insulation Board Install	14 days	Wed 8/10/11	Thu 8/25/11	11SS+5 days	
13	203(3) Unclassified Excavation	20 days	Thu 8/4/11	Fri 8/26/11	1,3SS+2 days	
14	618(2) Seeding	4 days	Sat 9/24/11	Wed 9/28/11	9,11,16,17	
15	203(5B) Manufacture Borrow, Type B	10 days	Sat 8/27/11	Wed 9/7/11	16SS-4 days	
16	203(5B) Hauling/Placing Borrow, Type B	13 days	Thu 9/1/11	Thu 9/15/11	11	
17	304(2) Subbase, Grading C	7 days	Fri 9/16/11	Fri 9/23/11	16	
18	643(3) Permanent Construction Signs	2 days	Thu 9/22/11	Fri 9/23/11	17FF	
19	642(4) Set Primary Monument	3 days	Sat 9/24/11	Tue 9/27/11	17	
20	642(12) Final Traverse	3 days	Sat 9/24/11	Tue 9/27/11	17	
21	640(1) Demobilization	1 day	Wed 8/1/12	Wed 8/1/12		



Project: Noorvik Schedule
Date: Fri 6/3/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

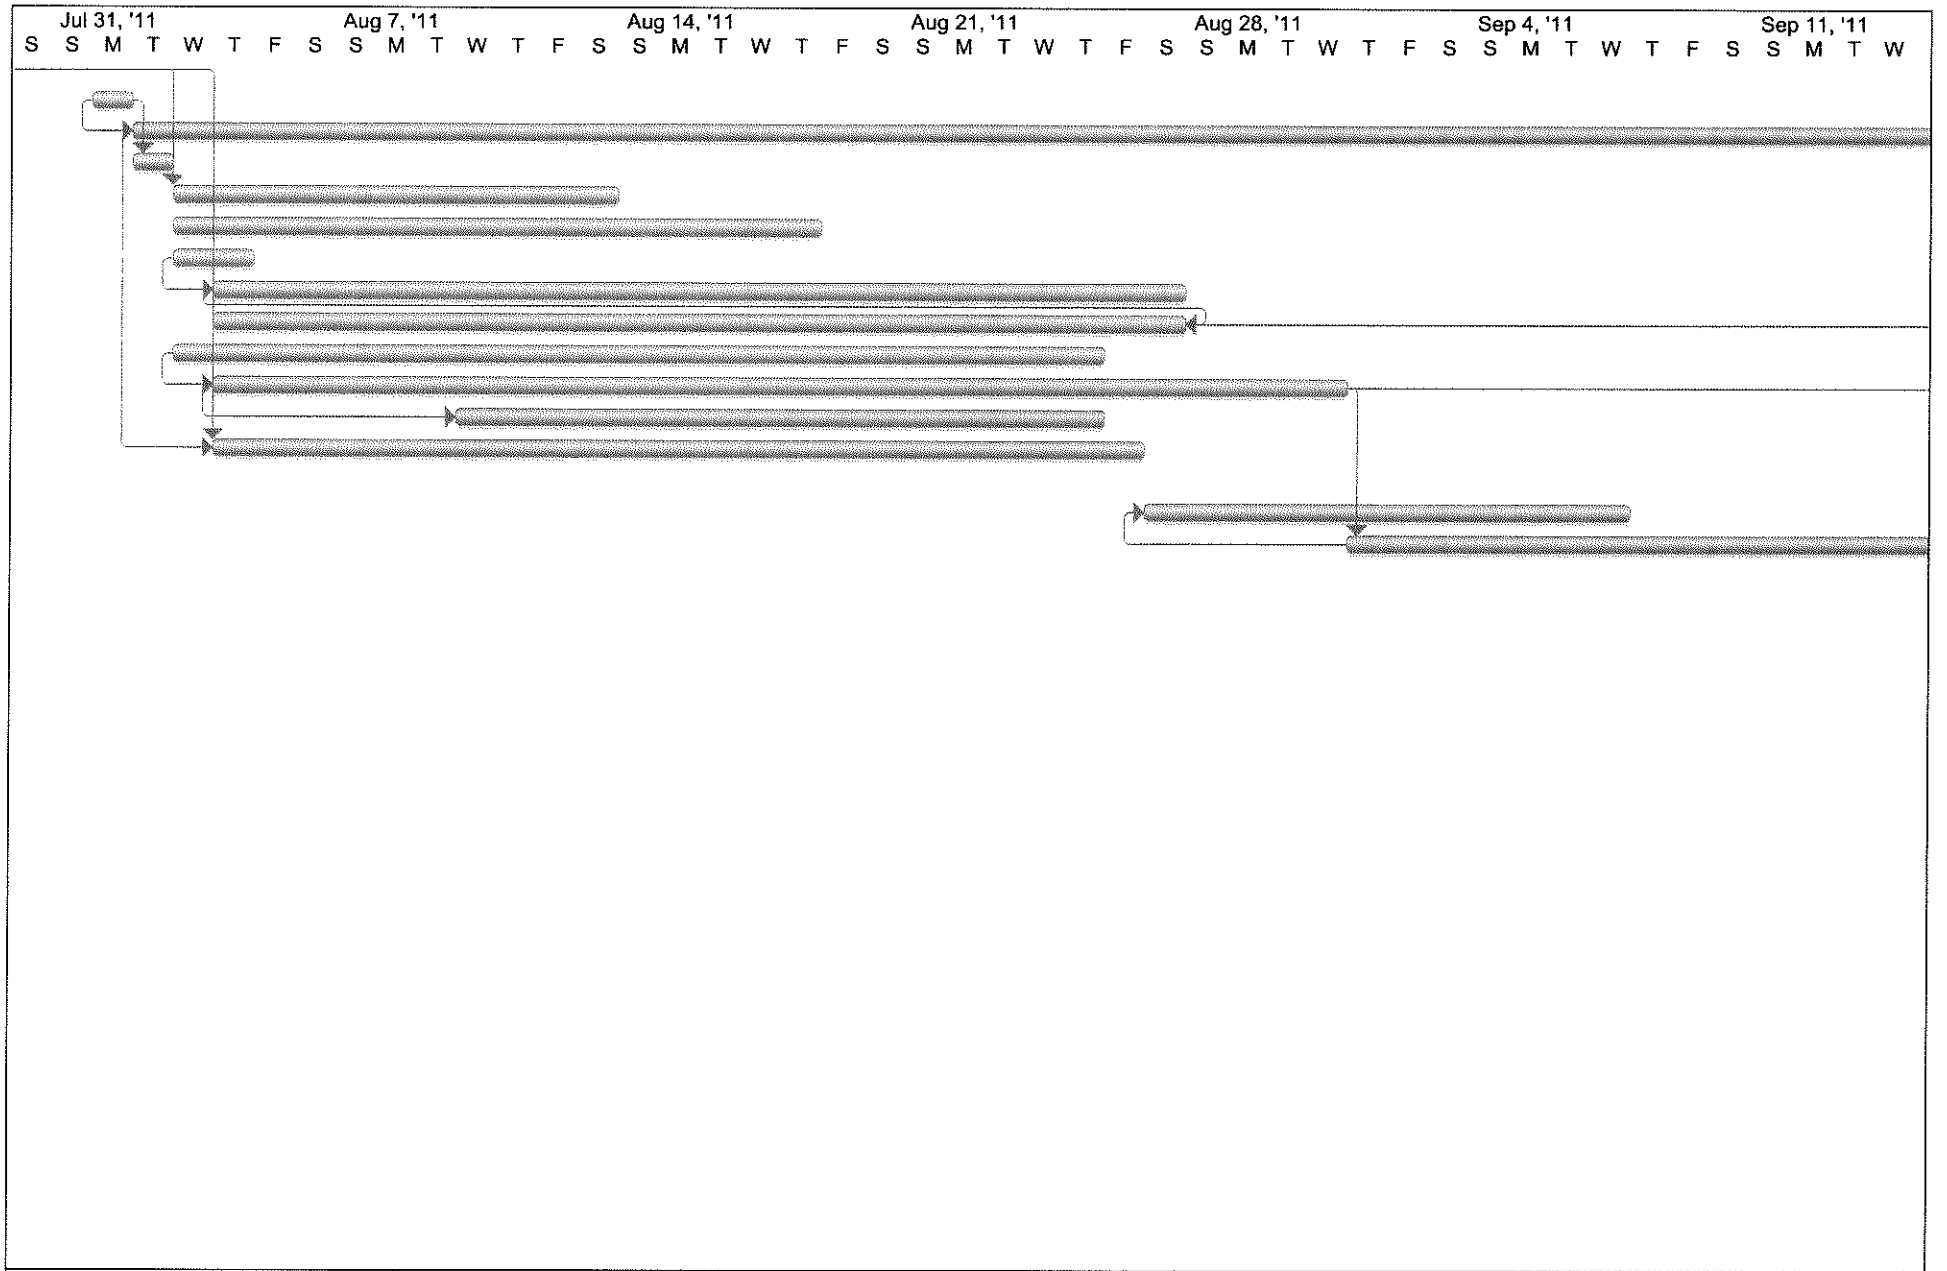

Project: Noorvik Schedule
Date: Fri 6/3/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

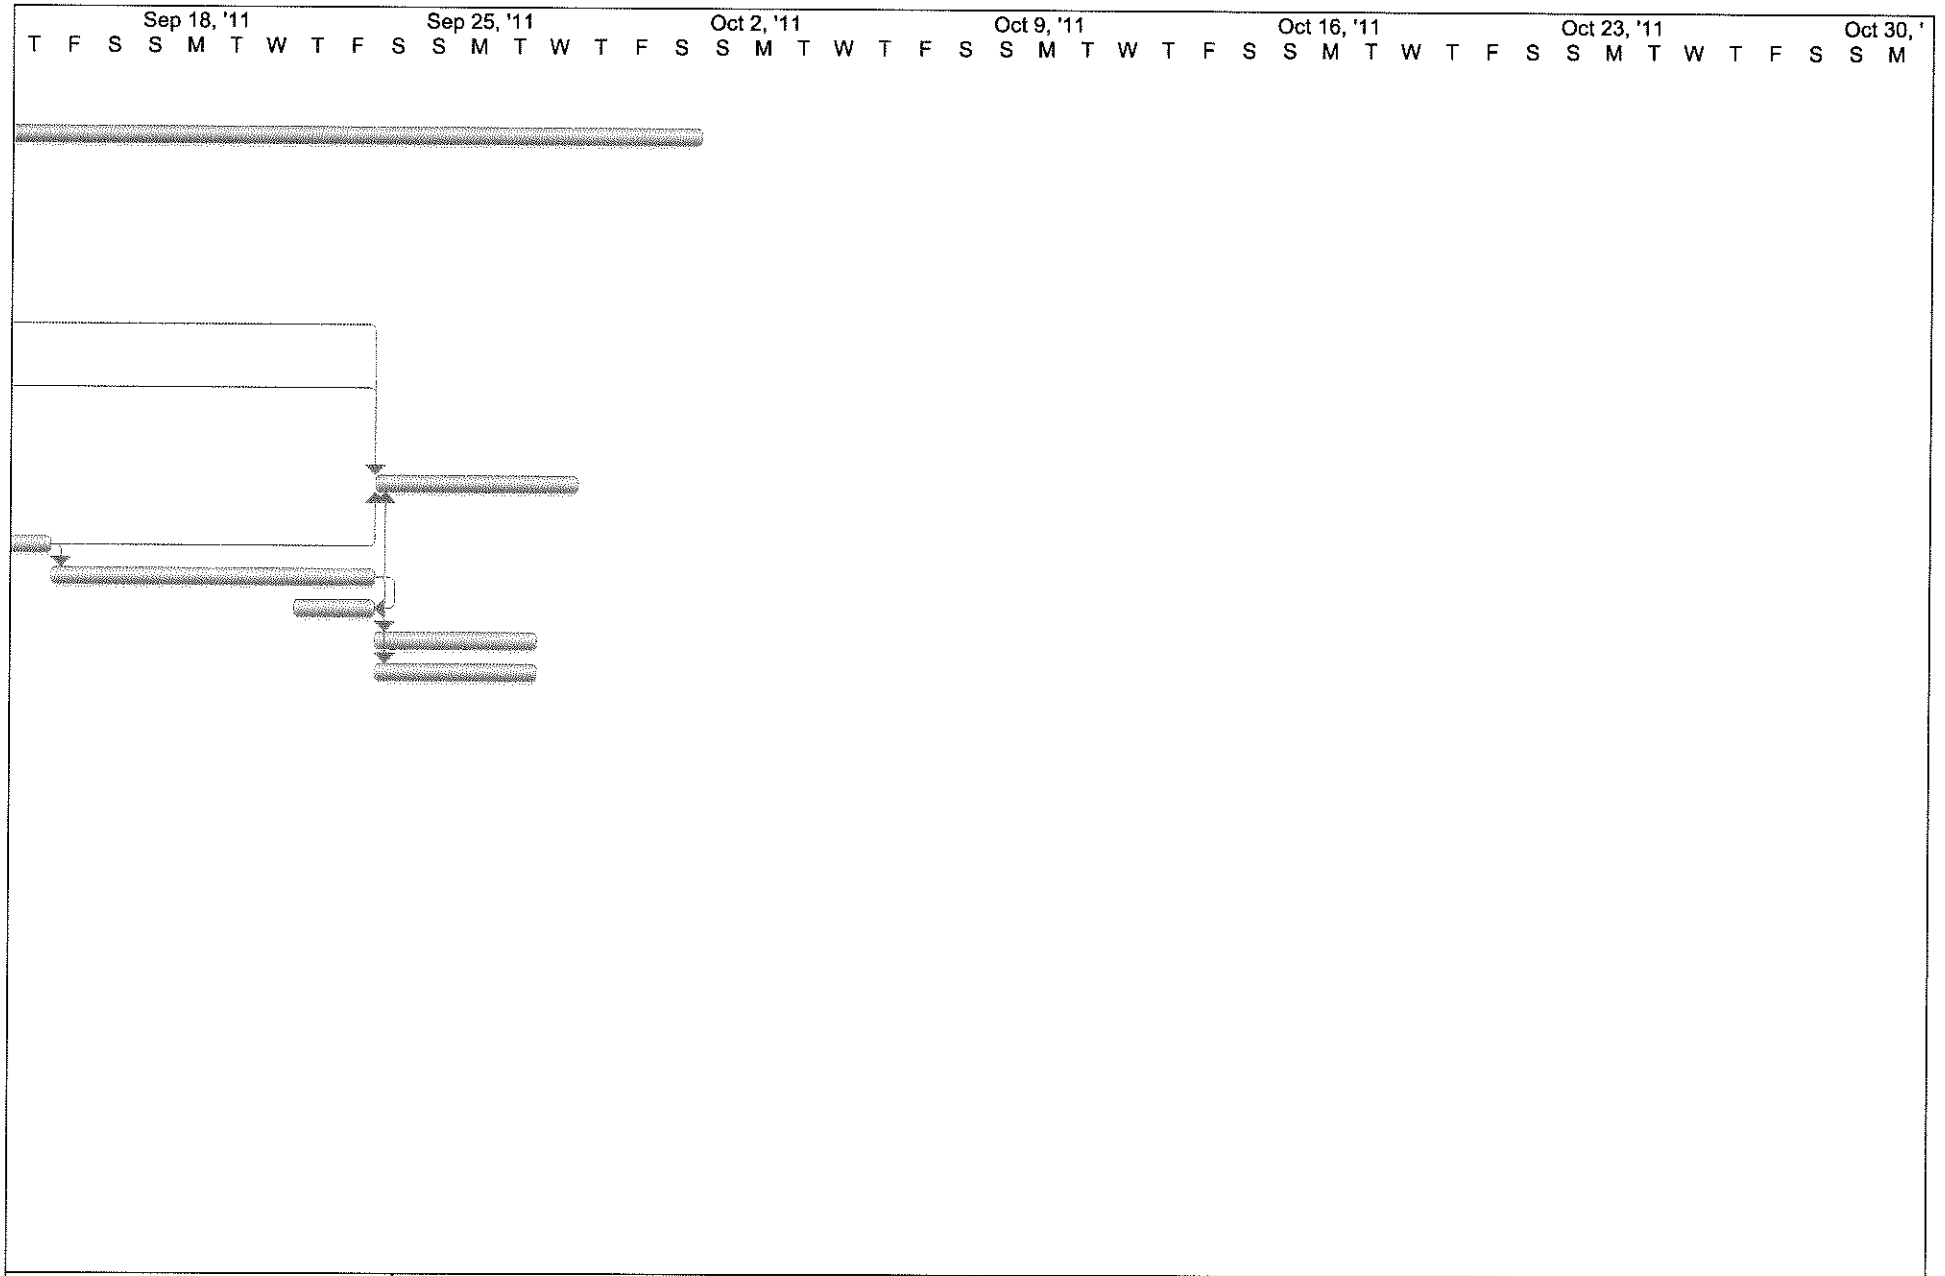

Project: Noorvik Schedule
Date: Fri 6/3/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
